



COMMITTEE ON JOINT SCHOOL BUILDINGS

July 9, 2024 at 5:00 PM

Aldermanic Chambers, City Hall (3rd Floor)

Members: Aldermen Terrio, Morgan, O'Neil
School Committee Members O'Connell, Soule, Turner

AGENDA

The Chairman calls the meeting to order.

The Clerk calls the roll.

1. Presentation from LeftField regarding the School District Priority One Project to date.
2. Monthly status and financial report for June 2024 submitted by LeftField.
If the Committee so desires, a motion is in order to accept the report and submit it to the Board of Mayor and Aldermen and Board of School Committee for informational purposes.

If there is no further business, a motion is in order to adjourn.



THE RIGHT CHOICE IN PROJECT MANAGEMENT

DRAFT

JSBC Meeting
July 9, 2024

TONIGHTS AGENDA

- 01 PROGRESS UPDATE
- 02 LOOK AHEAD ACTIVITIES
- 03 BUDGET & INVOICING
- 04 SCHEDULE
- 05 PROGRESS PICS
- 06 Q&A



Activities completed within the last 30-days

- Consigli Amendment/GMP executed
- Continued development and refinement of the Hillside & McLaughlin Schedules
- Continued programming for the Middle schools and Beech Elementary
- Utility infrastructure at the modular sites
- Continued scope coordination between Consigli and Triumph
- Continued coordination with Eversource for Modular power requirements
- Gas relocations complete at Parkside & Southside
- Continued move planning and coordination
- Continued communication with staff and the community
- Beech Elementary and Middle School Procurement
- Modular delivery and setting [95% complete]

DRAFT

30-Day Look-Ahead

- Continued development and refinement of the middle school schedules
- Continued CM procurement for the middle schools and Beech Elementary
- Continued Middle school and Beech Elementary programming
- Continued permit coordination
- Complete all utility work for the modular sites
- Site restoration as various modular sites
- Continue with interior fit-out for all modular units
- Continued coordination with Eversource for confirmation of lead time for pad mounted transformers
- Continued coordination for modular technology
- Start fiber cabling to the modulars
- Continued move planning
- Continued communication with all stakeholders



Priority 1 Projects | Update Summary

Priority One Projects	Project Phase					
	Programming	Design	CM Procured	Bidding	Construction	Closeout
Modulars	100%	100%	100%	100%	30%	0%
Beech	85%	20%	20%	0%	0%	0%
McLaughlin	95%	40%	40%	0%	0%	0%
Hillside	95%	40%	40%	0%	0%	0%
Parkside	85%	25%	40%	0%	0%	0%
Southside	50%	25%	40%	0%	0%	0%

DRAFT



Modulars Summary Update

Modulars	Project Phase									
	Modular Units Fabricated	Modular Units Infrastructure	Modulars Units Delivered	Modular Units Set	Modular Unit MEP, FA, PA Connections	General Sitework	Eversource Power	FA, Security, Certificate of Occupancy Testing	Modular Furniture, Equipment & Technology	Closeout
Beech	100%	100%	100%	100%	50%	85%	80%	0%	25%	0%
McDonough	100%	100%	100%	100%	35%	70%	60%	0%	25%	0%
McLaughlin	100%	100%	100%	100%	50%	85%	60%	0%	25%	0%
Hillside	100%	50%	0%	0%		50%	20%	0%	25%	0%
Parkside	100%	100%	100%	0%		50%	20%	0%	25%	0%
Southside	100%	100%	100%	100%		50%	20%	0%	25%	0%

DRAFT

Beech

- Receive & set Modulars
- Complete U/G electrical
- Sewer work and water line installed
- MEP, FA, PA ongoing

McDonough:

- U/G electrical work
- Retaining wall started
- Basketball hoops relocated
- Modulars delivered & set
- Utility work complete
- Prep expanded parking for paving work
- MEP, FA, PA work ongoing

McLaughlin

- Modular units delivered and set
- Skirting ongoing
- Paving [binder and curbing] complete
- Limited landscaping complete

Hillside

- Trench blasting completed
- Sewer work complete
- Awaiting delivery and set of modular units for week of July 8th

Southside

- Gas line relocated
- Modular units delivered at set
- MEP, FA, PA ongoing

Parkside:

- Modular pad complete
- Relocation of gas service complete
- Modular units delivered; setting is ongoing
- Water and sewer work completed



Eversource Summary Update

Modulars	Eversource Journey To Permanent Power						
	Site walk	Design	Pole Pad mounted	Work Orders Issued	Confirmation of Delivery *	Transformers, Cabinets ** Delivered	Power Terminated
Beech	100%	100%	Pole	100%	100%	100%	0%
McDonough	100%	100%	Pole	100%	100%	10%	0%
McLaughlin	100%	100%	Pole	100%	0%	20%	0%
Hillside	100%	100%	Pole	100%	0%	10%	0%
Parkside	100%	100%	Pole	100%	100%	0%	0%
Southside	100%	100%	Pole	100%	100%	10%	0%

* Estimated confirmation of lead times TBD.
** All CT cabinets have been delivered from Eversource



Manchester Priority One Projects - Overall Budget Summary

Manchester School District - Priority One Projects

Period Ending 5/31/2024
Invoice Summary Package 4



Current Budget



	Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	CTC (Actual committed)	Anticipated C @ C	Variance (Under) / Over
	[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	[I]	[J]=[D]+[I]	[K]=[C]-[J]
MODULAR PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$253,077	\$0	\$253,077	\$245,077	\$110,314	\$134,763	\$8,000	\$8,000	\$253,077	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$1,690,143	\$0	\$1,690,143	\$1,690,143	\$1,309,956	\$380,187	\$0	\$0	\$1,690,143	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$5,560,000	\$64,958	\$5,624,958	\$5,624,958	\$1,200,704	\$4,424,254	\$0	\$0	\$5,624,958	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$17,170,000	(\$213,195)	\$16,956,805	\$16,746,805	\$1,632,515	\$15,114,290	\$210,000	\$210,000	\$16,956,805	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$604,000	\$0	\$604,000	\$0	\$0	\$0	\$604,000	\$604,000	\$604,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$965,270	\$144,837	\$1,110,107	\$0	\$0	\$0	\$1,110,107	\$1,110,107	\$1,110,107	\$0
MODULAR PROJECT TOTALS	\$26,242,490	(\$3,400)	\$26,239,090	\$24,306,983	\$4,253,489	\$20,053,494	\$1,932,107	\$1,932,107	\$26,239,090	\$0
BEECH STREET ELEMENTARY SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$2,057,129	\$0	\$2,057,129	\$1,926,071	\$30,992	\$1,895,079	\$131,058	\$131,058	\$2,057,129	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$5,095,000	\$0	\$5,095,000	\$4,945,000	\$291,287	\$4,653,713	\$150,000	\$150,000	\$5,095,000	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$58,196,935	\$0	\$58,196,935	\$0	\$0	\$0	\$58,196,935	\$58,196,935	\$58,196,935	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$450,000	\$0	\$450,000	\$0	\$0	\$0	\$450,000	\$450,000	\$450,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$2,348,800	\$0	\$2,348,800	\$0	\$0	\$0	\$2,348,800	\$2,348,800	\$2,348,800	\$0
0800 0000 OWNER'S CONTINGENCY	\$5,963,970	(\$3,400)	\$5,960,570	\$0	\$0	\$0	\$5,960,570	\$5,960,570	\$5,960,570	\$0
BEECH STREET ELEMENTARY SCHOOL PROJECT TOTALS	\$74,111,834	(\$3,400)	\$74,108,434	\$1,971,071	\$322,279	\$6,548,792	\$67,237,363	\$67,237,363	\$74,108,434	\$0
HILLSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$33,340	\$943,285	\$40,529	\$40,529	\$1,017,155	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,087,500	\$0	\$4,087,500	\$3,937,500	\$305,743	\$3,631,757	\$150,000	\$150,000	\$4,087,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$43,527,708	\$0	\$43,527,708	\$0	\$0	\$0	\$43,527,708	\$43,527,708	\$43,527,708	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,520,000	\$0	\$3,520,000	\$0	\$0	\$0	\$3,520,000	\$3,520,000	\$3,520,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$4,601,489	(\$3,400)	\$4,598,089	\$0	\$0	\$0	\$4,598,089	\$4,598,089	\$4,598,089	\$0
HILLSIDE MIDDLE SCHOOL PROJECT TOTALS	\$57,003,852	(\$3,400)	\$57,000,452	\$4,914,126	\$339,083	\$4,575,042	\$52,086,326	\$52,086,326	\$57,000,452	\$0
MCLAUGHLIN MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$32,053	\$944,573	\$40,529	\$40,529	\$1,017,155	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,232,500	\$0	\$3,232,500	\$3,082,500	\$243,473	\$2,839,027	\$150,000	\$150,000	\$3,232,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$28,827,403	\$0	\$28,827,403	\$0	\$0	\$0	\$28,827,403	\$28,827,403	\$28,827,403	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$3,161,130	(\$3,400)	\$3,157,730	\$0	\$0	\$0	\$3,157,730	\$3,157,730	\$3,157,730	\$0
MCLAUGHLIN MIDDLE SCHOOL PROJECT TOTALS	\$39,688,188	(\$3,400)	\$39,684,788	\$4,059,126	\$275,526	\$3,783,600	\$35,625,662	\$35,625,662	\$39,684,788	\$0
PARKSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$35,663	\$1,021,718	\$43,907	\$43,907	\$1,101,287	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,927,500	\$0	\$3,927,500	\$3,777,500	\$38,400	\$3,739,100	\$150,000	\$150,000	\$3,927,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$36,146,140	\$0	\$36,146,140	\$0	\$0	\$0	\$36,146,140	\$36,146,140	\$36,146,140	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$3,877,019	(\$3,400)	\$3,873,619	\$0	\$0	\$0	\$3,873,619	\$3,873,619	\$3,873,619	\$0
PARKSIDE MIDDLE SCHOOL PROJECT TOTALS	\$48,501,946	(\$3,400)	\$48,498,546	\$4,834,881	\$74,063	\$4,760,818	\$43,663,666	\$43,663,666	\$48,498,546	\$0
SOUTHSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$33,450	\$1,023,930	\$43,907	\$43,907	\$1,101,287	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,317,500	\$0	\$4,317,500	\$4,167,500	\$43,200	\$4,124,300	\$150,000	\$150,000	\$4,317,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$46,685,769	\$0	\$46,685,769	\$0	\$0	\$0	\$46,685,769	\$46,685,769	\$46,685,769	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$4,893,735	(\$3,400)	\$4,890,335	\$0	\$0	\$0	\$4,890,335	\$4,890,335	\$4,890,335	\$0
SOUTHSIDE MIDDLE SCHOOL PROJECT TOTALS	\$60,451,691	(\$3,400)	\$60,448,291	\$5,224,881	\$76,650	\$5,148,230	\$55,223,411	\$55,223,411	\$60,448,291	\$0
PRIORITY ONE - DISTRICT WIDE COMMUNICATION	\$0	\$20,400	\$20,400	\$20,400	\$0	\$20,400	\$0	\$0	\$20,400	\$0
GRAND TOTAL MANCHESTER PRIORITY ONE PROJECTS	\$306,000,000	\$0	\$306,000,000	\$50,231,466	\$5,341,091	\$44,890,376	\$255,768,534	\$255,768,534	\$306,000,000	\$0

DRAFT



BUDGET STATUS – MOD PROJECT

Manchester School District - Modular Project



Manchester School District - Modular Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



	Original Budget [A]	Budget Reallocations [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (actual committed) [H]=[E]/[J]	CTC (actual committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$253,077	\$0	\$253,077	\$245,077	\$110,314	\$134,763	\$8,000		\$8,000	\$253,077	\$0
0101 0000 Legal Fees	\$8,000	\$0	\$8,000	\$0	\$0	\$0	\$8,000		\$8,000	\$8,000	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0400 Design Development	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0500 Construction Contract Docs	\$20,611	\$0	\$20,611	\$20,611	\$18,304	\$2,307	\$0	89%	\$0	\$20,611	\$0
0102 0600 Bidding	\$20,611	\$0	\$20,611	\$20,611	\$20,611	\$0	\$0	100%	\$0	\$20,611	\$0
0102 0700 Construction Contract Administration	\$203,855	\$0	\$203,855	\$203,855	\$71,399	\$132,456	\$0	35%	\$0	\$203,855	\$0
0102 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$1,690,143	\$0	\$1,690,143		\$1,309,956	\$380,187	\$0		\$0	\$1,690,143	\$0
0201 0000 Basic Services (SMMA)											
0201 0400 Design Development / Programming / RFP	\$216,000	\$0	\$216,000	\$216,000	\$216,000	\$0	\$0	100%	\$0	\$216,000	\$0
0201 0500 Construction Contract Documents / Site Package	\$480,000	\$0	\$480,000	\$480,000	\$480,000	\$0	\$0	100%	\$0	\$480,000	\$0
0201 0600 Bidding	\$96,000	\$0	\$96,000	\$96,000	\$96,000	\$0	\$0	100%	\$0	\$96,000	\$0
0201 0700 Construction Contract Administration	\$408,000	\$0	\$408,000	\$408,000	\$102,000	\$306,000	\$0	25%	\$0	\$408,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0300 GeoTechnical & Geo-Environmental	\$106,100	\$0	\$106,100	\$106,100	\$56,100	\$50,000	\$0	53%	\$0	\$106,100	\$0
0204 0400 Site Survey	\$365,750	\$0	\$365,750	\$365,750	\$359,856	\$5,894	\$0	98%	\$0	\$365,750	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$18,293	\$0	\$18,293	\$18,293	\$0	\$18,293	\$0	0%	\$0	\$18,293	\$0
0204 1200 Traffic Studies	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0300 0000 SITE ACQUISITION IN/AI	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$5,560,000	\$64,958	\$5,624,958	\$5,624,958	\$1,200,704	\$4,424,254	\$0		\$0	\$5,624,958	\$0
0501 0000 Pre-Construction Services	\$60,000	(\$44,640)	\$15,360	\$15,360	\$15,360	\$0	\$0	100%	\$0	\$15,360	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$5,500,000	\$109,598	\$5,609,598	\$5,609,598	\$1,185,344	\$4,424,254	\$0	21%	\$0	\$5,609,598	\$0
0508 0000 Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$17,170,000	(\$213,195)	\$16,956,805	\$16,746,805	\$1,632,515	\$15,114,290	\$210,000		\$210,000	\$16,956,805	\$0
0601 0000 Utility Company Fees	\$120,000	\$8,674	\$128,674	\$128,674	\$128,674	\$0	\$0	100%	\$0	\$128,674	\$0
0602 0000 Testing Services	\$50,000	(\$40,000)	\$10,000	\$0	\$0	\$0	\$10,000		\$10,000	\$10,000	\$0
0603 0000 Swing Space/Modulars	\$16,800,000	(\$134,184)	\$16,665,816	\$16,665,816	\$1,503,841	\$15,161,975	\$0	9%	\$0	\$16,665,816	\$0
0604 0000 Change Orders - Modulars	\$0	(\$47,685)	(\$47,685)	(\$47,685)	\$0	(\$47,685)	\$0	0%	\$0	(\$47,685)	\$0
0699 0000 Other Project Costs (Moving, etc.)	\$200,000	\$0	\$200,000	\$0	\$0	\$0	\$200,000		\$200,000	\$200,000	\$0
0699 0000 Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$604,000	\$0	\$604,000	\$0	\$0	\$0	\$604,000		\$604,000	\$604,000	\$0
0701 0000 Furnishings & Equipment (FF+E)	\$112,000	\$0	\$112,000	\$0	\$0	\$0	\$112,000		\$112,000	\$112,000	\$0
0703 0000 Technology	\$492,000	\$0	\$492,000	\$0	\$0	\$0	\$492,000		\$492,000	\$492,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$965,270	\$144,837	\$1,110,107	\$0	\$0	\$0	\$1,110,107		\$1,110,107	\$1,110,107	\$0
0801 0000 Owner's Contingency (soft)	\$163,958	(\$12,074)	\$151,884	\$0	\$0	\$0	\$151,884		\$151,884	\$151,884	\$0
0507 0000 Owner's Construction Contingency (hard)	\$801,312	\$156,911	\$958,223	\$0	\$0	\$0	\$958,223		\$958,223	\$958,223	\$0
PROJECT TOTALS	\$26,242,490	(\$3,400)	\$26,239,090	\$24,306,983	\$4,253,489	\$20,053,494	\$1,932,107		\$1,932,107	\$26,239,090	\$0

DRAFT



Invoice Summary for Period Ending June 2024

Please note that due to the timing of the meeting, warrant signing coordination, and invoice due dates, an invoice **DRAFT** will NOT be attached to this monthly report.

Page 10 of 53



Progress Pics



Beech Street Modular Units Set



Southside Modulares Being Set



McLaughlin Modular Set



McDonough Modulares Being Set



McDonough Parking Lot Prep Work



THANK YOU!

QUESTIONS & ANSWERS





MANCHESTER PRIORITY ONE PROJECTS

OPM Monthly Project Report

Period Ending June 2024

Prepared for:



Joint School Buildings Committee

Prepared by:



Priority One Projects - Progress Graph Summary

Priority One Projects	Project Phase					
	Programming	Design	CM Procured	Bidding	Construction	Closeout
Modulars	100%	100%	100%	100%	30%	0%
Beech	85%	20%	30%	0%	0%	0%
McLaughlin	95%	40%	40%	0%	0%	0%
Hillside	95%	40%	40%	0%	0%	0%
Parkside	85%	25%	40%	0%	0%	0%
Southside	50%	25%	40%	0%	0%	0%

I. EXECUTIVE SUMMARY

LeftField was officially engaged on February 20th and has since immersed itself in the Priority One projects, focusing on gaining institutional knowledge on the pre-existing Priority One schedule, budget, and documentation. That said, LeftField has been actively refining the budget and schedule to establish a LeftField project standard, which is attached to this report. Please note that while the overall budget of 306 million will not change; however, there will be budgetary reclasses of costs within individual projects and from project to project. Additionally, LeftField has developed a series of individual project schedules for each of the six Priority One projects and an overall Priority One schedule, which are also attached to this report. Similarly, to the budget, the schedules are subject to change. LeftField has also assisted with developing a Criminal History Record Inquiry (CHRI) process and badging system that would comply with the District's existing policies and the construction industry. To date, the CHRI process and badging system have been implemented. Regular meetings with the District are ongoing to ensure comprehensive discussion and coordination of all project aspects.

The modular project proceeded forward in June with continued coordination with Triumph Modular and Consigli Construction. The delivery of 72 modular units to Manchester remains on schedule, with the first arrival of modulars delivered on May 23rd, with the remaining to follow. As of the issuance of this report, all modular units have been fabricated, and the only remaining units are for Hillside, which are 100% fabricated and scheduled for delivery in the first & second week of July. Throughout July, Consigli Construction prepared sitework pads and utility work for the delivery of the modular units. Consigli and the project team continue weekly communication with Eversource regarding power coordination for the various modular sites, which remains a critical path element to the modular projects. Additionally, gas relocations were required at the Parkside and Southside project sites, which, as of the issuance of this report, have been completed.

LeftField has assisted the District with move coordination. Sterling Movers was retained by the District to manage the move from Wilson to the various modular locations. Throughout June, the District coordinated internal school moves with the assistance of the DPW through the vendors of Aramark and College Bound Movers. LeftField and SMMA continue to assist the District with technology relocation and procurement, which will continue throughout the summer months. Various project permitting has continued and will remain a focus for the Priority One Projects.

Programming continues for the Middle School Projects and Beech Elementary. CM procurement continues for the middle school projects and the Beech Elementary

School. The project team has met regularly to refine the schedules for the addition/renovations of the middle school projects, namely the Hillside and McLaughlin middle projects.

For further details, please refer to the additional project information provided in the various sections of this report.

II. PROJECT PROCUREMENT

Architect/Engineer Procurement:

SMMA has been issued various amendments to their base contract for continued work associated with the Priority One Projects.

Owner's Project Manager Procurement:

On February 20th, the District officially engaged LeftField as their Owner's Project Manager ("OPM"). LeftField's contract has been fully executed as of the issuance of this report.

CM Procurement for the Modulares:

CM procurement for the modular project was completed with the CM Agreement Contract executed with Consigli on April 4th. The GMP amendment was drafted, and the final revision was submitted for acceptance and executed on June 2nd. R.S. Audley Inc. will be the site contractor, and Longchamps Electric Inc. will be the electrical contractor. On June 24, 2024, general carpentry was awarded to North & South Construction Services.

Sterling Movers:

LeftField assisted the District with move coordination and recommended engaging the services of Sterling Movers for the various moves related to the modular project/ site locations. The District is currently coordinating the contract between Sterling and the District.

III. PROJECT ACTIVITIES COMPLETED DURING JUNE 2024

The following meetings/ Project activities occurred in June 2024:

- 06-04 Liberty gas coordination meeting
- 06-05 Attendance to seminar held by NH Department of Education re:
state funding
Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting

- 06-06 Weekly Project Meeting
- 06-06 Monthly Rpt 3 issued to the JSBC clerk
- 06-07 Monthly Rpt 3 and draft side deck issued to the JSBC
- 06-10 LeftField Team Weekly coordination meeting
- 06-11 Attendance to the JSBC meeting
- 06-12 Weekly Triumph Modular Coordination Meeting
- 06-12 Weekly Consigli meeting
- 06-12 Weekly Project Meeting
- 06-14 CM RFQ Statement of Qualifications received
- 06-17 LeftField Team Weekly coordination meeting
- 06-17 Attendance to Hillside Lower field & parking lot discussion
- 06-18 Internal LeftField coordination meeting to review CM SOQs
- 06-19 Weekly Triumph Modular Coordination Meeting
- 06-19 Weekly Consigli meeting
- 06-19 Weekly Project Meeting
- 06-19 Project Team meeting to coordinate middle school schedules
- 06-20 Beech Street planning option review meeting
- 06-20 Hillside utility coordination meeting
- 06-24 LeftField Team Weekly coordination meeting
- 06-26 Weekly Triumph Modular Coordination Meeting
- 06-26 Weekly Consigli meeting
- 06-26 Weekly Project Meeting
- 06-26 District review of CM SOQs
- 06-28 CMs notified of qualification status for the middle school projects

IV. ACTIVITIES PLANNED FOR JUNE 2024

The following meetings/ activities are planned for July 2024:

- 07-01 Internal weekly LeftField team coordination meeting
- 07-03 Weekly Triumph Modular Coordination Meeting
- 07-03 Weekly Consigli meeting
- 07-03 Issue monthly Rpt 3 and draft slide deck to the JSBC clerk
- 07-03 Middle School RFP issued to pre-qualified CMs
- 07-05 JSBC clerk issues monthly Rpt 3 and draft side deck to the JSBC
- 07-08 Internal LeftField Team Weekly coordination meeting
- 07-10 Weekly Triumph Modular Coordination Meeting
- 07-10 Weekly Consigli meeting
- 07-10 Weekly Project Meeting

- 07-15 LeftField Team Weekly coordination meeting
- 07-17 Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting
Weekly Project Meeting
- 07-22 LeftField Team Weekly coordination meeting
- 06-24 Weekly Triumph Modular Coordination Meeting
Weekly Consigli meeting
Weekly Project Meeting
- Final delivery and setting of Modulares [Hillside]
- Continued security coordination of Modulares
- Continued coordination of move activities
- Continued coordination of technology for the modulares

Please note additional activities and meetings will occur that have not been scheduled as of the issuance of this report. In addition, the above meetings are subject to change.

V. PROJECT BUDGET & INVOICING

LeftField has been forwarded the existing \$306M budget, previously established before LeftField's engagement. LeftField has developed and implemented the 306-million-dollar budget into a LeftField formatted standard. A summary of all six projects and individual project budgets can be found in Attachment A of this report. **Please note that this budget remains a work in progress. LeftField will be amending the budget based on a more thorough review of existing allocated project costs and anticipated project cost reallocations based on an individual budget line-item analysis.**

The recommended invoice approval process developed by LeftField and the District is working effectively, and billing and payment cycles have occurred to date. All invoices continue to be sent to LeftField and reviewed by the appropriate project team members. The contractor payment requisition is being reviewed by LeftField and SMMA and certified for payment by SMMA. LeftField has codified all invoices into a batch/ log with associated backup. The invoice log with backup is being signed as 'recommended for payment' by LeftField and issued to the District CFO and the Superintendent of Schools for signature. The CFO will then process payment accordingly based on the current schedule of Finance Warrant signing dates. **Please note that due to the timing of the JSBC meeting, warrant signing coordination, and invoice due dates, an invoice log will NOT be attached to this monthly report. However, as of the issuance of this report, we have attached an updated budget. Due to timing, not all invoices have been included as encumbered/expended.**

Change Orders Events to Date as of the Issuance of this Report:

Vendor	Value	Description
Triumph Modular		
PCO 2	\$(217,335)	Change from concrete footing system to metal plate foundation system
PCO 3	\$ 169,650	Associated grading and ramp changes
Subtotal	\$ (47,685)	This is reflective in the budget
Consigli Construction		
CO 1	\$ (21,539)	Finalization of alternates
Subtotal	\$ (21,539)	This will be reflective in the budget for next month
Total	\$ (69,224)	

VI. PROJECT SCHEDULE

LeftField has been developing the existing schedule. LeftField has transferred the received schedule into a LeftField formatted schedule. A summary of all six project schedules' rolled up' and individual project schedules can be found in Attachment C of this report. **Please note that the individual schedules and overall 'rolled up' schedule remains a work in progress. LeftField will be amending the individual project schedules based on a more thorough review of each individual project and anticipated scope.**

The modular project is currently on schedule. However, the availability and delivery of the Eversource pad-mounted transformers remain critical path activities.

Regarding the Middle School Projects, the project team has been meeting to review the timeline and phasing options for the middle school projects. **Based on the collective review and analysis by the project team, the Hillside & McLaughlin schedules have been further developed. As part of the period ending July 2024, these two project schedules will be updated and shared.**

Programming for the Middle Schools and Beech has continued throughout June.

MODULAR PROJECT

SUMMARY PROGRESS GRAPH

Modulars	Project Phase									
	Modular Units Fabricated	Modular Units Infrastructure	Modular Units Delivered	Modular Units Set	Modular Unit MEP, FA, PA Connections	General Sitework	Eversource Power	FA, Security, Certificate of Occupancy Testing	Modular Furniture, Equipment & Technology	Closeout
Beech	100%	100%	100%	100%	50%	85%	80%	0%	25%	0%
McDonough	100%	100%	100%	100%	35%	70%	60%	0%	25%	0%
McLaughlin	100%	100%	100%	100%	50%	85%	60%	0%	25%	0%
Hillside	100%	50%	0%	0%	0%	50%	20%	0%	25%	0%
Parkside	100%	100%	100%	0%	0%	50%	20%	0%	25%	0%
Southside	100%	100%	100%	100%	0%	50%	20%	0%	25%	0%

Modulars	Eversource Journey To Permanent Power						
	Site walk	Design	Pole Pad mounted	Work Orders Issued	Confirmation of Delivery *	Transformers, Cabinets ** Delivered	Power Terminated
Beech	100%	100%	Pole	100%	100%	100%	0%
McDonough	100%	100%	Pole	100%	100%	10%	0%
McLaughlin	100%	100%	Pad	100%	0%	20%	0%
Hillside	100%	100%	Pad	100%	0%	10%	0%
Parkside	100%	100%	Pole	100%	100%	0%	0%
Southside	100%	100%	Pole	100%	100%	10%	0%

* Estimated confirmation of lead times TBD.

** All CT cabinets have been delivered from Eversource

Construction-Related Activities During June 2024:

Beech

- Receive & set Modulars
- Complete U/G electrical
- Sewer work and water line installed
- MEP, FA, PA ongoing



Beech Street Modular Units Set

Southside

- Gas line relocated
- Modular units delivered at set
- MEP, FA, PA ongoing



Southside Modulares Being Set

Hillside

- Trench blasting completed
- Sewer work complete
- Awaiting delivery and set of modular units for week of July 8th

McLaughlin

- Modular units delivered and set
- Skirting ongoing
- Paving [binder and curbing] complete
- Limited landscaping complete



McLaughlin Modulares Set

Parkside:

- Modular pad complete
- Relocation of gas service complete
- Modular units delivered; setting is ongoing
- Water and sewer work completed

McDonough

- U/G electrical work
- Retaining wall started
- Basketball hoops relocated
- Modulares delivered & set
- Utility work complete
- Prep expanded parking for paving work
- MEP, FA, PA work ongoing



McDonough Modular Unit Set in Progress



McDonough Parking lot Prep-work

Next 30 days:Beech:

- Interior built-out
- MEP, FA, PA, security connections
- Final landscaping/hardscaping
- Modular skirting
- Modular ramps

McDonough:

- CT cabinet scheduled for installation week of July 1
- Pole-mounted transformer secured in Eversource yard
- Interior built-out
- MEP, FA, PA, security connections
- Limited landscaping/hardscaping
- Modular skirting

Hillside:

- Receive modulares and set
- Installation of water & electric
- Construction of temp parking lot and access road
- Interior built-out
- MEP, FA, PA, security connections
- Continued sitework

McLaughlin:

- Electrical shutdown TBD
- Interior built-out
- MEP, FA, PA, security connections
- Paving work to continue
- Modular skirting
- Finalization of sitework activities

Southside:

- Interior built-out
- MEP, FA, PA, security connections
- Paving work to continue
- Modular skirting
- Finalization of sitework activities

Parkside:

- Modulares are to be set in the first two weeks of July
- Interior built-out
- MEP, FA, PA, security connections
- Modular skirting
- Finalization of sitework activities

Middle School Projects

Upcoming Activities

- Issuance of the middle school RFP, receipt of proposals from qualified CM firms
- Ongoing schedule and phasing analysis for the middle school projects

Beech Elementary

Upcoming Activities

- CMR Procurement to continue
- Ongoing coordination of design options

VII. ATTACHMENTS

- Attachment A LeftField Budget [subject to further review & modifications]
- Attachment B N/A [see note in Section V – Project Budget & Invoicing]
- Attachment C LeftField Schedule [subject to further review & modifications]

VIII. PROJECT OUTREACH / COMMUNICATION

Project-related records such as agendas, agenda packets, and minutes can be viewed via this link:

<https://www.manchesternh.gov/Departments/City-Clerk/Meeting-Minutes-and-Agendas/Current>

Official upcoming meeting postings [date/time] can be viewed via this link:

<https://www.mansd.org/o/msd/page/calendar-bosc>
<https://www.manchesternh.gov/Government/City-Calendars>

ATTACHMENT A

Priority One Budget Rolled-Up Summary
Individual Project Budgets - Detail

Manchester Priority One Projects - Overall Budget Summary

Manchester School District - Priority One Projects

Period Ending
Invoice Summary Package

5/31/2024
4

Current Budget



	Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
MODULAR PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$253,077	\$0	\$253,077	\$245,077	\$110,314	\$134,763	\$8,000	\$8,000	\$253,077	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$1,690,143	\$0	\$1,690,143	\$1,690,143	\$1,309,956	\$380,187	\$0	\$0	\$1,690,143	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$5,560,000	\$64,958	\$5,624,958	\$5,624,958	\$1,200,704	\$4,424,254	\$0	\$0	\$5,624,958	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$17,170,000	(\$213,195)	\$16,956,805	\$16,746,805	\$1,632,515	\$15,114,290	\$210,000	\$210,000	\$16,956,805	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$604,000	\$0	\$604,000	\$0	\$0	\$0	\$604,000	\$604,000	\$604,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$965,270	\$144,837	\$1,110,107	\$0	\$0	\$0	\$1,110,107	\$1,110,107	\$1,110,107	\$0
MODULAR PROJECT TOTALS	\$26,242,490	(\$3,400)	\$26,239,090	\$24,306,983	\$4,253,489	\$20,053,494	\$1,932,107	\$1,932,107	\$26,239,090	\$0
BEECH STREET ELEMENTARY SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$2,057,129	\$0	\$2,057,129	\$1,926,071	\$30,992	\$1,895,079	\$131,058	\$131,058	\$2,057,129	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$5,095,000	\$0	\$5,095,000	\$4,945,000	\$291,287	\$4,653,713	\$150,000	\$150,000	\$5,095,000	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$58,196,935	\$0	\$58,196,935	\$0	\$0	\$0	\$58,196,935	\$58,196,935	\$58,196,935	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$450,000	\$0	\$450,000	\$0	\$0	\$0	\$450,000	\$450,000	\$450,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$2,348,800	\$0	\$2,348,800	\$0	\$0	\$0	\$2,348,800	\$2,348,800	\$2,348,800	\$0
0800 0000 OWNER'S CONTINGENCY	\$5,963,970	(\$3,400)	\$5,960,570	\$0	\$0	\$0	\$5,960,570	\$5,960,570	\$5,960,570	\$0
BEECH STREET ELEMENTARY SCHOOL PROJECT TOTALS	\$74,111,834	(\$3,400)	\$74,108,434	\$6,871,071	\$322,279	\$6,548,792	\$67,237,363	\$67,237,363	\$74,108,434	\$0
HILLSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$33,340	\$943,285	\$40,529	\$40,529	\$1,017,155	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,087,500	\$0	\$4,087,500	\$3,937,500	\$305,743	\$3,631,757	\$150,000	\$150,000	\$4,087,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$43,527,708	\$0	\$43,527,708	\$0	\$0	\$0	\$43,527,708	\$43,527,708	\$43,527,708	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,520,000	\$0	\$3,520,000	\$0	\$0	\$0	\$3,520,000	\$3,520,000	\$3,520,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$4,601,489	(\$3,400)	\$4,598,089	\$0	\$0	\$0	\$4,598,089	\$4,598,089	\$4,598,089	\$0
HILLSIDE MIDDLE SCHOOL PROJECT TOTALS	\$57,003,852	(\$3,400)	\$57,000,452	\$4,914,126	\$339,083	\$4,575,042	\$52,086,326	\$52,086,326	\$57,000,452	\$0
MCLAUGHLIN MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$32,053	\$944,573	\$40,529	\$40,529	\$1,017,155	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,232,500	\$0	\$3,232,500	\$3,082,500	\$243,473	\$2,839,027	\$150,000	\$150,000	\$3,232,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$28,827,403	\$0	\$28,827,403	\$0	\$0	\$0	\$28,827,403	\$28,827,403	\$28,827,403	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$3,161,130	(\$3,400)	\$3,157,730	\$0	\$0	\$0	\$3,157,730	\$3,157,730	\$3,157,730	\$0
MCLAUGHLIN MIDDLE SCHOOL PROJECT TOTALS	\$39,688,188	(\$3,400)	\$39,684,788	\$4,059,126	\$275,526	\$3,783,600	\$35,625,662	\$35,625,662	\$39,684,788	\$0
PARKSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$35,663	\$1,021,718	\$43,907	\$43,907	\$1,101,287	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,927,500	\$0	\$3,927,500	\$3,777,500	\$38,400	\$3,739,100	\$150,000	\$150,000	\$3,927,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$36,146,140	\$0	\$36,146,140	\$0	\$0	\$0	\$36,146,140	\$36,146,140	\$36,146,140	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$3,877,019	(\$3,400)	\$3,873,619	\$0	\$0	\$0	\$3,873,619	\$3,873,619	\$3,873,619	\$0
PARKSIDE MIDDLE SCHOOL PROJECT TOTALS	\$48,501,946	(\$3,400)	\$48,498,546	\$4,834,881	\$74,063	\$4,760,818	\$43,663,666	\$43,663,666	\$48,498,546	\$0
SOUTHSIDE MIDDLE SCHOOL PROJECT										
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,101,287	\$0	\$1,101,287	\$1,057,381	\$33,450	\$1,023,930	\$43,907	\$43,907	\$1,101,287	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$4,317,500	\$0	\$4,317,500	\$4,167,500	\$43,200	\$4,124,300	\$150,000	\$150,000	\$4,317,500	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$46,685,769	\$0	\$46,685,769	\$0	\$0	\$0	\$46,685,769	\$46,685,769	\$46,685,769	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$4,897,135	(\$3,400)	\$4,893,735	\$0	\$0	\$0	\$4,893,735	\$4,893,735	\$4,893,735	\$0
SOUTHSIDE MIDDLE SCHOOL PROJECT TOTALS	\$60,451,691	(\$3,400)	\$60,448,291	\$5,224,881	\$76,650	\$5,148,230	\$55,223,411	\$55,223,411	\$60,448,291	\$0
PRIORITY ONE - DISTRICT WIDE COMMUNICATION	\$0	\$20,400	\$20,400	\$20,400	\$0	\$20,400	\$0	\$0	\$20,400	\$0
GRAND TOTAL MANCHESTER PRIORITY ONE PROJECTS	\$306,000,000	\$0	\$306,000,000	\$50,231,466	\$5,341,091	\$44,890,376	\$255,768,534	\$255,768,534	\$306,000,000	\$0

Manchester School District - Modular Project



Manchester School District - Modular Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



	Original Budget [A]	Budget Reallocations [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against commit't'd) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$253,077	\$0	\$253,077	\$245,077	\$110,314	\$134,763	\$8,000		\$8,000	\$253,077	\$0
0101 0000 Legal Fees	\$8,000	\$0	\$8,000	\$0	\$0	\$0	\$8,000		\$8,000	\$8,000	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0400 Design Development	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0500 Construction Contract Docs	\$20,611	\$0	\$20,611	\$20,611	\$18,304	\$2,307	\$0	89%	\$0	\$20,611	\$0
0102 0600 Bidding	\$20,611	\$0	\$20,611	\$20,611	\$20,611	\$0	\$0	100%	\$0	\$20,611	\$0
0102 0700 Construction Contract Administration	\$203,855	\$0	\$203,855	\$203,855	\$71,399	\$132,456	\$0	35%	\$0	\$203,855	\$0
0102 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$1,690,143	\$0	\$1,690,143	\$1,690,143	\$1,309,956	\$380,187	\$0		\$0	\$1,690,143	\$0
0201 0000 Basic Services (SMMA)											
0201 0400 Design Development / Programming / RFP	\$216,000	\$0	\$216,000	\$216,000	\$216,000	\$0	\$0	100%	\$0	\$216,000	\$0
0201 0500 Construction Contract Documents / Site Package	\$480,000	\$0	\$480,000	\$480,000	\$480,000	\$0	\$0	100%	\$0	\$480,000	\$0
0201 0600 Bidding	\$96,000	\$0	\$96,000	\$96,000	\$96,000	\$0	\$0	100%	\$0	\$96,000	\$0
0201 0700 Construction Contract Administration	\$408,000	\$0	\$408,000	\$408,000	\$102,000	\$306,000	\$0	25%	\$0	\$408,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0300 GeoTechnical & Geo-Environmental	\$106,100	\$0	\$106,100	\$106,100	\$56,100	\$50,000	\$0	53%	\$0	\$106,100	\$0
0204 0400 Site Survey	\$365,750	\$0	\$365,750	\$365,750	\$359,856	\$5,894	\$0	98%	\$0	\$365,750	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$18,293	\$0	\$18,293	\$18,293	\$0	\$18,293	\$0	0%	\$0	\$18,293	\$0
0204 1200 Traffic Studies	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0300 0000 SITE ACQUISITION [N/A]	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$5,560,000	\$64,958	\$5,624,958	\$5,624,958	\$1,200,704	\$4,424,254	\$0		\$0	\$5,624,958	\$0
0501 0000 Pre-Construction Services	\$60,000	(\$44,640)	\$15,360	\$15,360	\$15,360	\$0	\$0	100%	\$0	\$15,360	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$5,500,000	\$109,598	\$5,609,598	\$5,609,598	\$1,185,344	\$4,424,254	\$0	21%	\$0	\$5,609,598	\$0
0508 0000 Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0600 0000 MISCELLANEOUS PROJECT COSTS	\$17,170,000	(\$213,195)	\$16,956,805	\$16,746,805	\$1,632,515	\$15,114,290	\$210,000		\$210,000	\$16,956,805	\$0
0601 0000 Utility Company Fees	\$120,000	\$8,674	\$128,674	\$128,674	\$128,674	\$0	\$0	100%	\$0	\$128,674	\$0
0602 0000 Testing Services	\$50,000	(\$40,000)	\$10,000	\$0	\$0	\$0	\$10,000		\$10,000	\$10,000	\$0
0603 0000 Swing Space/Modulars	\$16,800,000	(\$134,184)	\$16,665,816	\$16,665,816	\$1,503,841	\$15,161,975	\$0	9%	\$0	\$16,665,816	\$0
0604 0000 Change Orders - Modulars	\$0	(\$47,685)	(\$47,685)	(\$47,685)	\$0	(\$47,685)	\$0	0%	\$0	(\$47,685)	\$0
0699 0000 Other Project Costs (Moving, etc.)	\$200,000	\$0	\$200,000	\$0	\$0	\$0	\$200,000		\$200,000	\$200,000	\$0
0699 0000 Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700 0000 FURNISHINGS & EQUIPMENT	\$604,000	\$0	\$604,000	\$0	\$0	\$0	\$604,000		\$604,000	\$604,000	\$0
0701 0000 Furnishings & Equipment (FF+E)	\$112,000	\$0	\$112,000	\$0	\$0	\$0	\$112,000		\$112,000	\$112,000	\$0
0703 0000 Technology	\$492,000	\$0	\$492,000	\$0	\$0	\$0	\$492,000		\$492,000	\$492,000	\$0
0800 0000 OWNER'S CONTINGENCY	\$965,270	\$144,837	\$1,110,107	\$0	\$0	\$0	\$1,110,107		\$1,110,107	\$1,110,107	\$0
0801 0000 Owner's Contingency (soft)	\$163,958	(\$12,074)	\$151,884	\$0	\$0	\$0	\$151,884		\$151,884	\$151,884	\$0
0507 0000 Owner's Construction Contingency (hard)	\$801,312	\$156,911	\$958,223	\$0	\$0	\$0	\$958,223		\$958,223	\$958,223	\$0
PROJECT TOTALS	\$26,242,490	(\$3,400)	\$26,239,090	\$24,306,983	\$4,253,489	\$20,053,494	\$1,932,107		\$1,932,107	\$26,239,090	\$0

Manchester School District - Beech Street Elementary School Project



Manchester School District - Beech Street Elementary School Project
Project Director / Manager: David Saindon / Hamdi Cobanoglu

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget

	Original Budget [A]	Budget Changes [B]	Current Budget [C]	Committed Costs [D]	Expended [E]	Unspent [F]=[D]-[E]	Remaining Budget [G]=[C]-[D]	% Complete (against committd) [H]=[E]/[J]	CTC (beyond committed) [I]	Anticipated C @ C [J]=[D]+[I]	Variance (Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION	\$2,057,129	\$0	\$2,057,129	\$1,926,071	\$30,992	\$1,895,079	\$131,058				
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Feasibility/Schematic Design	\$173,979	\$0	\$173,979	\$173,979	\$30,992	\$142,987	\$0	18%	\$0	\$173,979	\$0
0102 0400 Design Development	\$74,563	\$0	\$74,563	\$74,563	\$0	\$74,563	\$0	0%	\$0	\$74,563	\$0
0102 0500 Construction Contract Docs	\$99,417	\$0	\$99,417	\$99,417	\$0	\$99,417	\$0	0%	\$0	\$99,417	\$0
0102 0600 Bidding	\$50,055	\$0	\$50,055	\$50,055	\$0	\$50,055	\$0	0%	\$0	\$50,055	\$0
0102 0700 Construction Contract Administration	\$1,546,243	\$0	\$1,546,243	\$1,465,185	\$0	\$1,465,185	\$81,058	0%	\$81,058	\$1,546,243	\$0
0102 0800 Closeout	\$62,872	\$0	\$62,872	\$62,872	\$0	\$62,872	\$0	0%	\$0	\$62,872	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (Cookson Communications)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100 Cost Estimates	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$5,095,000	\$0	\$5,095,000	\$4,945,000	\$291,287	\$4,653,713	\$150,000				
0201 0000 Basic Services (SMMA)											
0201 0100 Feasibility/Schematic Design	\$819,000	\$0	\$819,000	\$819,000	\$245,700	\$573,300	\$0	30%	\$0	\$819,000	\$0
0201 0400 Design Development	\$819,000	\$0	\$819,000	\$819,000	\$0	\$819,000	\$0	0%	\$0	\$819,000	\$0
0201 0500 Construction Contract Documents	\$1,228,500	\$0	\$1,228,500	\$1,228,500	\$0	\$1,228,500	\$0	0%	\$0	\$1,228,500	\$0
0201 0600 Bidding	\$204,750	\$0	\$204,750	\$204,750	\$0	\$204,750	\$0	0%	\$0	\$204,750	\$0
0201 0700 Construction Contract Administration	\$1,023,750	\$0	\$1,023,750	\$1,023,750	\$0	\$1,023,750	\$0	0%	\$0	\$1,023,750	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$50,000	\$0	\$50,000	\$50,000	\$0	\$50,000	\$0	0%	\$0	\$50,000	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$225,000	\$0	\$225,000	\$225,000	\$0	\$225,000	\$0	0%	\$0	\$225,000	\$0
0204 0300 GeoTechnical & Geo-Environmental (H&A)	\$300,000	\$0	\$300,000	\$300,000	\$24,970	\$275,030	\$0	8%	\$0	\$300,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies (BSC)	\$125,000	\$0	\$125,000	\$125,000	\$20,617	\$104,383	\$0	16%	\$0	\$125,000	\$0
0300 0000 SITE ACQUISITION	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$58,196,935	\$0	\$58,196,935	\$0	\$0	\$0	\$58,196,935		\$58,196,935	\$58,196,935	\$0
0501 0000 Pre-Construction Services	\$275,000	\$0	\$275,000	\$0	\$0	\$0	\$275,000		\$275,000	\$275,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$37,789,750	\$0	\$37,789,750	\$0	\$0	\$0	\$37,789,750		\$37,789,750	\$37,789,750	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$1,590,400	\$0	\$1,590,400	\$0	\$0	\$0	\$1,590,400		\$1,590,400	\$1,590,400	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Beech Street Elementary School Project



Manchester School District - Beech Street Elementary School Project
Project Director / Manager: David Saindon / Hamdi Cobanoglu

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



			Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated C @ C	Variance
			[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	[J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0502	0400	Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 5 - Metals											
0502	0500	Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0600	Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 7 - Thermal and Moisture Protection											
0502	0700	Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Waterproofing & Damproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 8 - Openings											
0502	0800	Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 9 - Finishes											
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0900	Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1000	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 11 - Equipment											
0502	1100	Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1200	Division 12 - Furnishings											
		Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1400	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2100	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2200	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2300	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2600	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	3100	Division 31 - Earthwork	\$10,986,750	\$0	\$10,986,750	\$0	\$0	\$0	\$10,986,750		\$10,986,750	\$10,986,750	\$0
0502	3200	Division 32 - Exterior Improvements (Carried in Earthwork)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509	0000	Design/Pricing Contingency	\$7,555,035	\$0	\$7,555,035	\$0	\$0	\$0	\$7,555,035		\$7,555,035	\$7,555,035	\$0
0600	0000	MISCELLANEOUS PROJECT COSTS	\$450,000	\$0	\$450,000	\$0	\$0	\$0	\$450,000		\$450,000	\$450,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$150,000	\$0	\$150,000	\$0	\$0	\$0	\$150,000		\$150,000	\$150,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$200,000	\$0	\$200,000	\$0	\$0	\$0	\$200,000		\$200,000	\$200,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700	0000	FURNISHINGS & EQUIPMENT	\$2,348,800	\$0	\$2,348,800	\$0	\$0	\$0	\$2,348,800		\$2,348,800	\$2,348,800	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,174,400	\$0	\$1,174,400	\$0	\$0	\$0	\$1,174,400		\$1,174,400	\$1,174,400	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000	Technology	\$1,174,400	\$0	\$1,174,400	\$0	\$0	\$0	\$1,174,400		\$1,174,400	\$1,174,400	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800	0000	OWNER'S CONTINGENCY	\$5,963,970	(\$3,400)	\$5,960,570	\$0	\$0	\$0	\$5,960,570		\$5,960,570	\$5,960,570	\$0
0801	0000	Owner's Contingency (soft)	\$828,684	(\$3,400)	\$824,684	\$0	\$0	\$0	\$824,684		\$824,684	\$824,684	\$0
0507	0000	Owner's Construction Contingency (hard)	\$5,135,886	\$0	\$5,135,886	\$0	\$0	\$0	\$5,135,886		\$5,135,886	\$5,135,886	\$0
PROJECT TOTALS			\$74,111,834	(\$3,400)	\$74,108,434	\$6,871,071	\$322,279	\$6,548,792	\$67,237,363		\$67,237,363	\$74,108,434	\$0

Manchester School District - Hillside Middle School Project



Manchester School District - Hillside Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



		Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete (against commit'd)	CTC (beyond committed)	Anticipated C @ C	Variance (Under) / Over
		[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	[H]=[E]/[J]	[I]	[J]=[D]+[I]	[K]=[C]-[J]
0100 0000	ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$33,340	\$943,285	\$40,529		\$40,529	\$1,017,155	\$0
0101 0000	Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000	Owner's Project Manager (Leftfield)											
0102 0100	Programming/Schematic Design	\$76,728	\$0	\$76,728	\$76,728	\$33,340	\$43,387	\$0	43%	\$0	\$76,728	\$0
0102 0400	Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	\$0	0%	\$0	\$57,546	\$0
0102 0500	Construction Contract Docs	\$172,182	\$0	\$172,182	\$172,182	\$0	\$172,182	\$0	0%	\$0	\$172,182	\$0
0102 0600	Bidding	\$66,909	\$0	\$66,909	\$66,909	\$0	\$66,909	\$0	0%	\$0	\$66,909	\$0
0102 0700	Construction Contract Administration	\$609,254	\$0	\$609,254	\$568,725	\$0	\$568,725	\$40,529	0%	\$40,529	\$609,254	\$0
0102 0800	Closeout	\$34,537	\$0	\$34,537	\$34,537	\$0	\$34,537	\$0	0%	\$0	\$34,537	\$0
0102 0900	Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000	Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100	Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900	Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000	Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000	Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000	Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000	ARCHITECTURE & ENGINEERING	\$4,087,500	\$0	\$4,087,500	\$3,937,500	\$305,743	\$3,631,757	\$150,000		\$150,000	\$4,087,500	\$0
0201 0000	Basic Services (SMMA)											
0201 0100	Programming/Schematic Design	\$612,000	\$0	\$612,000	\$612,000	\$255,000	\$357,000	\$0	42%	\$0	\$612,000	\$0
0201 0400	Design Development	\$748,000	\$0	\$748,000	\$748,000	\$0	\$748,000	\$0	0%	\$0	\$748,000	\$0
0201 0500	Construction Contract Documents	\$1,020,000	\$0	\$1,020,000	\$1,020,000	\$0	\$1,020,000	\$0	0%	\$0	\$1,020,000	\$0
0201 0600	Bidding	\$170,000	\$0	\$170,000	\$170,000	\$0	\$170,000	\$0	0%	\$0	\$170,000	\$0
0201 0700	Construction Contract Administration	\$850,000	\$0	\$850,000	\$850,000	\$0	\$850,000	\$0	0%	\$0	\$850,000	\$0
0201 0800	Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900	Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000	Reimbursable and Other Services											
0203 0200	Printing (over minimum)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Other Reimbursable Costs (consultant contingency)	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	\$0	0%	\$0	\$12,500	\$0
0203 9900	Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Permitting - Transportation	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000	Sub-Consultants											
0204 0200	Hazardous Materials	\$150,000	\$0	\$150,000	\$150,000	\$0	\$150,000	\$0	0%	\$0	\$150,000	\$0
0204 0300	GeoTechnical & Geo-Environmental (H&A)	\$125,000	\$0	\$125,000	\$125,000	\$37,620	\$87,380	\$0	30%	\$0	\$125,000	\$0
0204 0400	Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500	Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200	Traffic Studies (BSC)	\$100,000	\$0	\$100,000	\$100,000	\$13,123	\$86,877	\$0	13%	\$0	\$100,000	\$0
0300 0000	SITE ACQUISITION [N/A]	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000	Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000	Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000	Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000	CONSTRUCTION CONTRACT	\$43,527,708	\$0	\$43,527,708	\$0	\$0	\$0	\$43,527,708		\$43,527,708	\$43,527,708	\$0
0501 0000	Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0502 0000	Construction											
0502 0000	Construction Budget	\$34,063,224	\$0	\$34,063,224	\$0	\$0	\$0	\$34,063,224		\$34,063,224	\$34,063,224	\$0
0502 0010	GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020	GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030	CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100	Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100	Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200	Division 2 - Existing Conditions											
0502 0200	Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Hillside Middle School Project



Manchester School District - Hillside Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



		Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
		[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	C @ C [J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0502 0300	Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400	Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500	Division 5 - Metals											\$0
	Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600	Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0700	Division 7 - Thermal and Moisture Protection											
	Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Waterproofing & Damproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0800	Division 8 - Openings											
	Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0900	Division 9 - Finishes											
	Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 1000	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Division 11 - Equipment											
0502 1100	Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 1200	Division 12 - Furnishings											
	Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 1400	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2100	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2200	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2300	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2600	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 3100	Division 31 - Earthwork	\$3,700,000	\$0	\$3,700,000	\$0	\$0	\$0	\$3,700,000		\$3,700,000	\$3,700,000	\$0
0502 3200	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 9900	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506 0000	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508 0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509 0000	Design/Pricing Contingency	\$5,664,484	\$0	\$5,664,484	\$0	\$0	\$0	\$5,664,484		\$5,664,484	\$5,664,484	\$0
0600 0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601 0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602 0000	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603 0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699 0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699 0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700 0000	FURNISHINGS & EQUIPMENT	\$3,520,000	\$0	\$3,520,000	\$0	\$0	\$0	\$3,520,000		\$3,520,000	\$3,520,000	\$0
0701 0000	Furnishings & Equipment (FF+E)	\$1,760,000	\$0	\$1,760,000	\$0	\$0	\$0	\$1,760,000		\$1,760,000	\$1,760,000	\$0
0702 0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703 0000	Technology	\$1,760,000	\$0	\$1,760,000	\$0	\$0	\$0	\$1,760,000		\$1,760,000	\$1,760,000	\$0
0799 0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800 0000	OWNER'S CONTINGENCY	\$4,601,489	(\$3,400)	\$4,598,089	\$0	\$0	\$0	\$4,598,089		\$4,598,089	\$4,598,089	\$0
0801 0000	Owner's Contingency (soft)	\$713,393	(\$3,400)	\$709,993	\$0	\$0	\$0	\$709,993		\$709,993	\$709,993	\$0
0507 0000	Owner's Construction Contingency (hard)	\$3,888,096	\$0	\$3,888,096	\$0	\$0	\$0	\$3,888,096		\$3,888,096	\$3,888,096	\$0
PROJECT TOTALS		\$57,003,852	(\$3,400)	\$57,000,452	\$4,914,126	\$339,083	\$4,575,042	\$52,086,326		\$52,086,326	\$57,000,452	\$0

Manchester School District - McLaughlin Middle School Project



Manchester School District - McLaughlin Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



	Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated C @ C	Variance
	[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	[J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0100 0000 ADMINISTRATION (OPM & OTHER ADMIN. COSTS)	\$1,017,155	\$0	\$1,017,155	\$976,626	\$32,053	\$944,573	\$40,529		\$40,529	\$1,017,155	\$0
0101 0000 Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 0000 Owner's Project Manager (Leftfield)											
0102 0100 Programming/Schematic Design	\$76,728	\$0	\$76,728	\$76,728	\$32,053	\$44,675	\$0	42%	\$0	\$76,728	\$0
0102 0400 Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	\$0	0%	\$0	\$57,546	\$0
0102 0500 Construction Contract Docs	\$172,182	\$0	\$172,182	\$172,182	\$0	\$172,182	\$0	0%	\$0	\$172,182	\$0
0102 0600 Bidding	\$66,909	\$0	\$66,909	\$66,909	\$0	\$66,909	\$0	0%	\$0	\$66,909	\$0
0102 0700 Construction Contract Administration	\$609,254	\$0	\$609,254	\$568,725	\$0	\$568,725	\$40,529	0%	\$40,529	\$609,254	\$0
0102 0800 Closeout	\$34,537	\$0	\$34,537	\$34,537	\$0	\$34,537	\$0	0%	\$0	\$34,537	\$0
0102 0900 Extra Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000 Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100 Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900 Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000 Advertising	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000 Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000 Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000 Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000 ARCHITECTURE & ENGINEERING	\$3,232,500	\$0	\$3,232,500	\$3,082,500	\$243,473	\$2,839,027	\$150,000		\$150,000	\$3,232,500	\$0
0201 0000 Basic Services (SMMA)											
0201 0100 Programming/Schematic Design	\$468,000	\$0	\$468,000	\$468,000	\$195,000	\$273,000	\$0	42%	\$0	\$468,000	\$0
0201 0400 Design Development	\$572,000	\$0	\$572,000	\$572,000	\$0	\$572,000	\$0	0%	\$0	\$572,000	\$0
0201 0500 Construction Contract Documents	\$780,000	\$0	\$780,000	\$780,000	\$0	\$780,000	\$0	0%	\$0	\$780,000	\$0
0201 0600 Bidding	\$130,000	\$0	\$130,000	\$130,000	\$0	\$130,000	\$0	0%	\$0	\$130,000	\$0
0201 0700 Construction Contract Administration	\$650,000	\$0	\$650,000	\$650,000	\$0	\$650,000	\$0	0%	\$0	\$650,000	\$0
0201 0800 Closeout	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900 Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000 Reimbursable and Other Services											
0203 0200 Printing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Other Reimbursable Costs	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	\$0	0%	\$0	\$12,500	\$0
0203 9900 Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Permitting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Con-Com	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Stormwater	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900 FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000 Sub-Consultants											
0204 0200 Hazardous Materials	\$100,000	\$0	\$100,000	\$100,000	\$0	\$100,000	\$0	0%	\$0	\$100,000	\$0
0204 0300 GeoTechnical & Geo-Environmental (H&A)	\$120,000	\$0	\$120,000	\$120,000	\$33,220	\$86,780	\$0	28%	\$0	\$120,000	\$0
0204 0400 Site Survey	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500 Wetlands	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200 Traffic Studies (BSC)	\$100,000	\$0	\$100,000	\$100,000	\$15,253	\$84,747	\$0	15%	\$0	\$100,000	\$0
0300 0000 SITE ACQUISITION [N/A]	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0301 0000 Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000 Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000 Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000 CONSTRUCTION CONTRACT	\$28,827,403	\$0	\$28,827,403	\$0	\$0	\$0	\$28,827,403		\$28,827,403	\$28,827,403	\$0
0501 0000 Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0502 0000 Construction											
0502 0000 Construction Budget	\$20,080,350	\$0	\$20,080,350	\$0	\$0	\$0	\$20,080,350		\$20,080,350	\$20,080,350	\$0
0502 0010 GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020 GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030 CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100 Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200 Division 2 - Existing Conditions											
0502 0200 Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0300 Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - McLaughlin Middle School Project



Manchester School District - McLaughlin Middle School Project
Project Director / Manager: David Saindon / Mark Lenfest

Period Ending
Invoice Summary Package
Includes GC/CM Requisition

5/31/2024
4
N/A

Current Budget



			Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated C @ C	Variance
			[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(H)=[E]/[J]	(I)	(J)=[D]+[I]	(K)=[C]-[J]
0502	0400	Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Division 5 - Metals											
0502	0500	Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	0600	Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Division 7 - Thermal and Moisture Protection											
0502	0700	Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Division 8 - Openings											
0502	0800	Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Division 9 - Finishes											
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	0900	Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	1000	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Division 11 - Equipment											
0502	1100	Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
		Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	1200	Division 12 - Furnishings											
		Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	1400	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2100	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2200	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2300	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	2600	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	3100	Division 31 - Earthwork	\$4,900,000	\$0	\$4,900,000	\$0	\$0	\$0	\$4,900,000	\$4,900,000	\$4,900,000	\$4,900,000	\$0
0502	3200	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0502	9900	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0506	0000	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0508	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0509	0000	Design/Pricing Contingency	\$3,747,053	\$0	\$3,747,053	\$0	\$0	\$0	\$3,747,053	\$3,747,053	\$3,747,053	\$3,747,053	\$0
0600	0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000	\$250,000	\$250,000	\$250,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000	\$100,000	\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000	\$50,000	\$50,000	\$50,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000	\$100,000	\$100,000	\$100,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0700	0000	FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000	\$3,200,000	\$3,200,000	\$3,200,000	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000	\$1,600,000	\$1,600,000	\$1,600,000	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0703	0000	Technology	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000	\$1,600,000	\$1,600,000	\$1,600,000	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0800	0000	OWNER'S CONTINGENCY	\$3,161,130	(\$3,400)	\$3,157,730	\$0	\$0	\$0	\$3,157,730	\$3,157,730	\$3,157,730	\$3,157,730	\$0
0801	0000	Owner's Contingency (soft)	\$507,181	(\$3,400)	\$503,781	\$0	\$0	\$0	\$503,781	\$503,781	\$503,781	\$503,781	\$0
0507	0000	Owner's Construction Contingency (hard)	\$2,653,949	\$0	\$2,653,949	\$0	\$0	\$0	\$2,653,949	\$2,653,949	\$2,653,949	\$2,653,949	\$0
PROJECT TOTALS			\$39,688,188	(\$3,400)	\$39,684,788	\$4,059,126	\$275,526	\$3,783,600	\$35,625,662		\$35,625,662	\$39,684,788	\$0

Manchester School District - Parkside Middle School Project



Manchester School District - Parkside Middle School Project
Project Director / Manager: David Saindon / Linda Lipoto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



	Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
	[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd)	(beyond committed)	C @ C	(Under) / Over
								[H]=[E]/[J]	[I]	[J]=[D]+[I]	[K]=[C]-[J]
0100 0000	ADMINISTRATION (OPM & OTHER ADMIN. COSTS)										
0101 0000	Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0
0102 0000	Owner's Project Manager (Leftfield)										
0102 0100	Programming/Schematic Design	\$72,469	\$0	\$72,469	\$69,091	\$35,663	\$33,428	52%	\$3,378	\$72,469	\$0
0102 0400	Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	0%	\$0	\$57,546	\$0
0102 0500	Construction Contract Docs	\$115,092	\$0	\$115,092	\$115,092	\$0	\$115,092	0%	\$0	\$115,092	\$0
0102 0600	Bidding	\$52,637	\$0	\$52,637	\$52,637	\$0	\$52,637	0%	\$0	\$52,637	\$0
0102 0700	Construction Contract Administration	\$763,016	\$0	\$763,016	\$735,997	\$0	\$735,997	0%	\$27,019	\$763,016	\$0
0102 0800	Closeout	\$40,529	\$0	\$40,529	\$27,019	\$0	\$27,019	0%	\$13,510	\$40,529	\$0
0102 0900	Extra Services	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000	Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100	Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900	Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000	Advertising	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000	Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000	Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000	ARCHITECTURE & ENGINEERING										
0201 0000	Basic Services										
0201 0100	Programming/Schematic Design	\$576,000	\$0	\$576,000	\$576,000	\$38,400	\$537,600	7%	\$0	\$576,000	\$0
0201 0400	Design Development	\$704,000	\$0	\$704,000	\$704,000	\$0	\$704,000	0%	\$0	\$704,000	\$0
0201 0500	Construction Contract Documents	\$960,000	\$0	\$960,000	\$960,000	\$0	\$960,000	0%	\$0	\$960,000	\$0
0201 0600	Bidding	\$160,000	\$0	\$160,000	\$160,000	\$0	\$160,000	0%	\$0	\$160,000	\$0
0201 0700	Construction Contract Administration	\$800,000	\$0	\$800,000	\$800,000	\$0	\$800,000	0%	\$0	\$800,000	\$0
0201 0800	Closeout	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900	Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000	Reimbursable and Other Services										
0203 0200	Printing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Other Reimbursable Costs	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	0%	\$0	\$12,500	\$0
0203 9900	Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Permitting	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Permitting	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Con-Com	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Stormwater	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000	Sub-Consultants										
0204 0200	Hazardous Materials	\$175,000	\$0	\$175,000	\$175,000	\$0	\$175,000	0%	\$0	\$175,000	\$0
0204 0300	GeoTechnical & Geo-Environmental	\$140,000	\$0	\$140,000	\$140,000	\$0	\$140,000	0%	\$0	\$140,000	\$0
0204 0400	Site Survey	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500	Wetlands	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200	Traffic Studies	\$100,000	\$0	\$100,000	\$100,000	\$0	\$100,000	0%	\$0	\$100,000	\$0
0300 0000	SITE ACQUISITION [NA]										
0301 0000	Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000	Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000	Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000	CONSTRUCTION CONTRACT										
0501 0000	Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0		\$100,000	\$100,000	\$0
0502 0000	Construction										
0502 0000	Construction Budget	\$24,538,450	\$0	\$24,538,450	\$0	\$0	\$0		\$24,538,450	\$24,538,450	\$0
0502 0010	GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020	GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030	CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100	Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100	Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200	Division 2 - Existing Conditions										
0502 0200	Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Parkside Middle School Project



Manchester School District - Parkside Middle School Project
Project Director / Manager: David Saindon / Linda Lipoto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



			Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
			[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit'd) [H]=[E]/[J]	(beyond committed) [I]	C @ C [J]=[D]+[I]	(Under) / Over [K]=[C]-[J]
0502 0300	Division 3 - Concrete		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0400	Division 4 - Masonry		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0500	Division 5 - Metals												\$0
	Structural Steel		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Misc. Metals		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0600	Division 6 - Wood, Plastics and Composites (Finish Carpentry)		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0700	Division 7 - Thermal and Moisture Protection												
	Metal Panels		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Roofing		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Waterproofing & Damproofing		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0800	Division 8 - Openings												
	Metal Windows		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Hollow Metal Doors, Frames, Hardware		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Special Doors		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Glass & Glazing		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0900	Division 9 - Finishes												
	Metal Studs and Drywall		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Tiling		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Acoustical Ceilings		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Wood Flooring		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Carpet/Resilient Flooring		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Resinous Flooring		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 1000	Division 10 - Specialties		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Signage		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Division 11 - Equipment												
0502 1100	Stage Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Food Service Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
	Athletic Equipment		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 1200	Division 12 - Furnishings												
	Window Treatments		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 1400	Division 14 - Conveying Systems (Elevators)		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2100	Division 21 - Fire Suppression		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2200	Division 22 - Plumbing		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2300	Division 23 - HVAC		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 2600	Division 26 - Electrical		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 3100	Division 31 - Earthwork	\$5,500,000	\$0	\$0	\$5,500,000	\$0	\$0	\$0	\$5,500,000		\$5,500,000	\$5,500,000	\$0
0502 3200	Division 32 - Exterior Improvements (Landscaping)		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 9900	Retainage		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506 0000	Alternates		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508 0000	Change Orders		\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509 0000	Design/Pricing Contingency	\$6,007,690	\$0	\$0	\$6,007,690	\$0	\$0	\$0	\$6,007,690		\$6,007,690	\$6,007,690	\$0
0600 0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$0	\$250,000	\$0	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601 0000	Utility Company Fees	\$100,000	\$0	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602 0000	Testing Services	\$50,000	\$0	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603 0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699 0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699 0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700 0000	FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000		\$3,200,000	\$3,200,000	\$0
0701 0000	Furnishings & Equipment (FF+E)	\$1,600,000	\$0	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0702 0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703 0000	Technology	\$1,600,000	\$0	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0799 0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800 0000	OWNER'S CONTINGENCY	\$3,877,019	(\$3,400)	\$0	\$3,873,619	\$0	\$0	\$0	\$3,873,619		\$3,873,619	\$3,873,619	\$0
0801 0000	Owner's Contingency (soft)	\$608,899	(\$3,400)	\$0	\$605,499	\$0	\$0	\$0	\$605,499		\$605,499	\$605,499	\$0
0507 0000	Owner's Construction Contingency (hard)	\$3,268,120	\$0	\$0	\$3,268,120	\$0	\$0	\$0	\$3,268,120		\$3,268,120	\$3,268,120	\$0
PROJECT TOTALS			\$48,501,946	(\$3,400)	\$48,498,546	\$4,834,881	\$74,063	\$4,760,818	\$43,663,666		\$43,663,666	\$48,498,546	\$0

Manchester School District - Southside Middle School Project



Manchester School District - Southside Middle School Project
Project Director / Manager: David Saindon / Linda Liporto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



	Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated	Variance
	[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit't'd)	(beyond committed)	C @ C	(Under) / Over
								[H]=[E]/[J]	[I]	[J]=[D]*[I]	[K]=[C]-[J]
0100 0000	ADMINISTRATION (OPM & OTHER ADMIN. COSTS)										
0101 0000	Legal Fees	\$0	\$0	\$0	\$0	\$0	\$0			\$0	\$0
0102 0000	Owner's Project Manager (Leftfield)										
0102 0100	Programming/Schematic Design	\$72,469	\$0	\$72,469	\$69,091	\$33,450	\$35,641	48%	\$3,378	\$72,469	\$0
0102 0400	Design Development	\$57,546	\$0	\$57,546	\$57,546	\$0	\$57,546	0%	\$0	\$57,546	\$0
0102 0500	Construction Contract Docs	\$115,092	\$0	\$115,092	\$115,092	\$0	\$115,092	0%	\$0	\$115,092	\$0
0102 0600	Bidding	\$52,637	\$0	\$52,637	\$52,637	\$0	\$52,637	0%	\$0	\$52,637	\$0
0102 0700	Construction Contract Administration	\$763,016	\$0	\$763,016	\$735,997	\$0	\$735,997	0%	\$27,019	\$763,016	\$0
0102 0800	Closeout	\$40,529	\$0	\$40,529	\$27,019	\$0	\$27,019	0%	\$13,510	\$40,529	\$0
0102 0900	Extra Services	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1000	Reimbursable & Other Services (A&A Move Management)	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 1100	Cost Estimates	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0102 9900	Other Project Manager Costs	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0103 0000	Advertising	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0104 0000	Permitting Fees	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0105 0000	Owner's Insurance	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Other Administrative Costs	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Structural Peer Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Scope of Site Plan & Special Permit Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Test Pit Observations	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Stormwater Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0199 0000	Fire Alarm/Life Safety Peer Review	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0200 0000	ARCHITECTURE & ENGINEERING										
0201 0000	Basic Services (SMMA)										
0201 0100	Programming/Schematic Design	\$648,000	\$0	\$648,000	\$648,000	\$43,200	\$604,800	7%	\$0	\$648,000	\$0
0201 0400	Design Development	\$792,000	\$0	\$792,000	\$792,000	\$0	\$792,000	0%	\$0	\$792,000	\$0
0201 0500	Construction Contract Documents	\$1,080,000	\$0	\$1,080,000	\$1,080,000	\$0	\$1,080,000	0%	\$0	\$1,080,000	\$0
0201 0600	Bidding	\$180,000	\$0	\$180,000	\$180,000	\$0	\$180,000	0%	\$0	\$180,000	\$0
0201 0700	Construction Contract Administration	\$900,000	\$0	\$900,000	\$900,000	\$0	\$900,000	0%	\$0	\$900,000	\$0
0201 0800	Closeout	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0201 9900	Other Basic Services	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 0000	Reimbursable and Other Services										
0203 0200	Printing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Other Reimbursable Costs	\$12,500	\$0	\$12,500	\$12,500	\$0	\$12,500	0%	\$0	\$12,500	\$0
0203 9900	Other Misc. Reimbursable Costs	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Permitting	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Soil Testing	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Hydrant Flow Test	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Con-Com	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Stormwater	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	Noise Survey	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0203 9900	FF&E/Technology Design	\$300,000	\$0	\$300,000	\$150,000	\$0	\$150,000	0%	\$150,000	\$300,000	\$0
0204 0000	Sub-Consultants										
0204 0200	Hazardous Materials	\$175,000	\$0	\$175,000	\$175,000	\$0	\$175,000	0%	\$0	\$175,000	\$0
0204 0300	GeoTechnical & Geo-Environmental	\$130,000	\$0	\$130,000	\$130,000	\$0	\$130,000	0%	\$0	\$130,000	\$0
0204 0400	Site Survey	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 0500	Wetlands	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0204 1200	Traffic Studies	\$100,000	\$0	\$100,000	\$100,000	\$0	\$100,000	0%	\$0	\$100,000	\$0
0300 0000	SITE ACQUISITION										
0301 0000	Land/Building Purchase	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0302 0000	Appraisal Fees	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0303 0000	Recording Fees	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0500 0000	CONSTRUCTION CONTRACT										
0501 0000	Pre-Construction Services	\$100,000	\$0	\$100,000	\$0	\$0	\$0		\$100,000	\$100,000	\$0
0502 0000	Construction										
0502 0000	Construction Budget	\$35,121,474	\$0	\$35,121,474	\$0	\$0	\$0		\$35,121,474	\$35,121,474	\$0
0502 0010	GMP - Fee	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0020	GMP - Insurances	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0030	CM Contingency	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100	Division 1 - General Conditions	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0100	Division 1 - General Requirements	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0200	Division 2 - Existing Conditions										
0502 0200	Demolition/Abatement	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502 0300	Division 3 - Concrete	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0

Manchester School District - Southside Middle School Project



Manchester School District - Southside Middle School Project
Project Director / Manager: David Saindon / Linda Lipoto

Period Ending 5/31/2024
Invoice Summary Package 4
Includes GC/CM Requisition N/A

Current Budget



			Original Budget	Budget Changes	Current Budget	Committed Costs	Expended	Unspent	Remaining Budget	% Complete	CTC	Anticipated C @ C	Variance
			[A]	[B]	[C]	[D]	[E]	[F]=[D]-[E]	[G]=[C]-[D]	(against commit't'd) [H]=[E]/[J]	(beyond committed) [I]	[J]=[D]*[I]	(Under) / Over [K]=[C]-[J]
0502	0400	Division 4 - Masonry	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0500	Division 5 - Metals											
		Structural Steel	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Misc. Metals	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0600	Division 6 - Wood, Plastics and Composites (Finish Carpentry)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 7 - Thermal and Moisture Protection											
0502	0700	Metal Panels	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Roofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Waterproofing & Dampproofing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 8 - Openings											
0502	0800	Metal Windows	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Hollow Metal Doors, Frames, Hardware	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Special Doors	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Glass & Glazing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 9 - Finishes											
		Metal Studs and Drywall	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Tiling	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	0900	Acoustical Ceilings	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Wood Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Carpet/Resilient Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Resinous Flooring	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Painting	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1000	Division 10 - Specialties	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Signage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Division 11 - Equipment											
0502	1100	Stage Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Food Service Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
		Athletic Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1200	Division 12 - Furnishings											
		Window Treatments	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	1400	Division 14 - Conveying Systems (Elevators)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2100	Division 21 - Fire Suppression	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2200	Division 22 - Plumbing	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2300	Division 23 - HVAC	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	2600	Division 26 - Electrical	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	3100	Division 31 - Earthwork	\$3,700,000	\$0	\$3,700,000	\$0	\$0	\$0	\$3,700,000		\$3,700,000	\$3,700,000	\$0
0502	3200	Division 32 - Exterior Improvements (Landscaping)	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0502	9900	Retainage	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0506	0000	Alternates	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0508	0000	Change Orders	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0509	0000	Design/Pricing Contingency	\$7,764,295	\$0	\$7,764,295	\$0	\$0	\$0	\$7,764,295		\$7,764,295	\$7,764,295	\$0
0600	0000	MISCELLANEOUS PROJECT COSTS	\$250,000	\$0	\$250,000	\$0	\$0	\$0	\$250,000		\$250,000	\$250,000	\$0
0601	0000	Utility Company Fees	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0602	0000	Testing Services	\$50,000	\$0	\$50,000	\$0	\$0	\$0	\$50,000		\$50,000	\$50,000	\$0
0603	0000	Swing Space/Modulars	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0699	0000	Other Project Costs (Moving, etc.)	\$100,000	\$0	\$100,000	\$0	\$0	\$0	\$100,000		\$100,000	\$100,000	\$0
0699	0000	Stipend for Teacher Move	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0700	0000	FURNISHINGS & EQUIPMENT	\$3,200,000	\$0	\$3,200,000	\$0	\$0	\$0	\$3,200,000		\$3,200,000	\$3,200,000	\$0
0701	0000	Furnishings & Equipment (FF+E)	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0702	0000	Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0703	0000	Technology	\$1,600,000	\$0	\$1,600,000	\$0	\$0	\$0	\$1,600,000		\$1,600,000	\$1,600,000	\$0
0799	0000	Other Furnishings & Equipment	\$0	\$0	\$0	\$0	\$0	\$0	\$0		\$0	\$0	\$0
0800	0000	OWNER'S CONTINGENCY	\$4,897,135	(\$3,400)	\$4,893,735	\$0	\$0	\$0	\$4,893,735		\$4,893,735	\$4,893,735	\$0
0801	0000	Owner's Contingency (soft)	\$752,980	(\$3,400)	\$749,580	\$0	\$0	\$0	\$749,580		\$749,580	\$749,580	\$0
0507	0000	Owner's Construction Contingency (hard)	\$4,144,155	\$0	\$4,144,155	\$0	\$0	\$0	\$4,144,155		\$4,144,155	\$4,144,155	\$0
PROJECT TOTALS			\$60,451,691	(\$3,400)	\$60,448,291	\$5,224,881	\$76,650	\$5,148,230	\$55,223,411		\$55,223,411	\$60,448,291	\$0

ATTACHMENT B


Invoice Log For Reporting Period


NOT APPLICABLE THIS MONTH

See notes in Section V

ATTACHMENT C

Priority One Schedule Rolled-Up
Individual Project Schedules – Detail

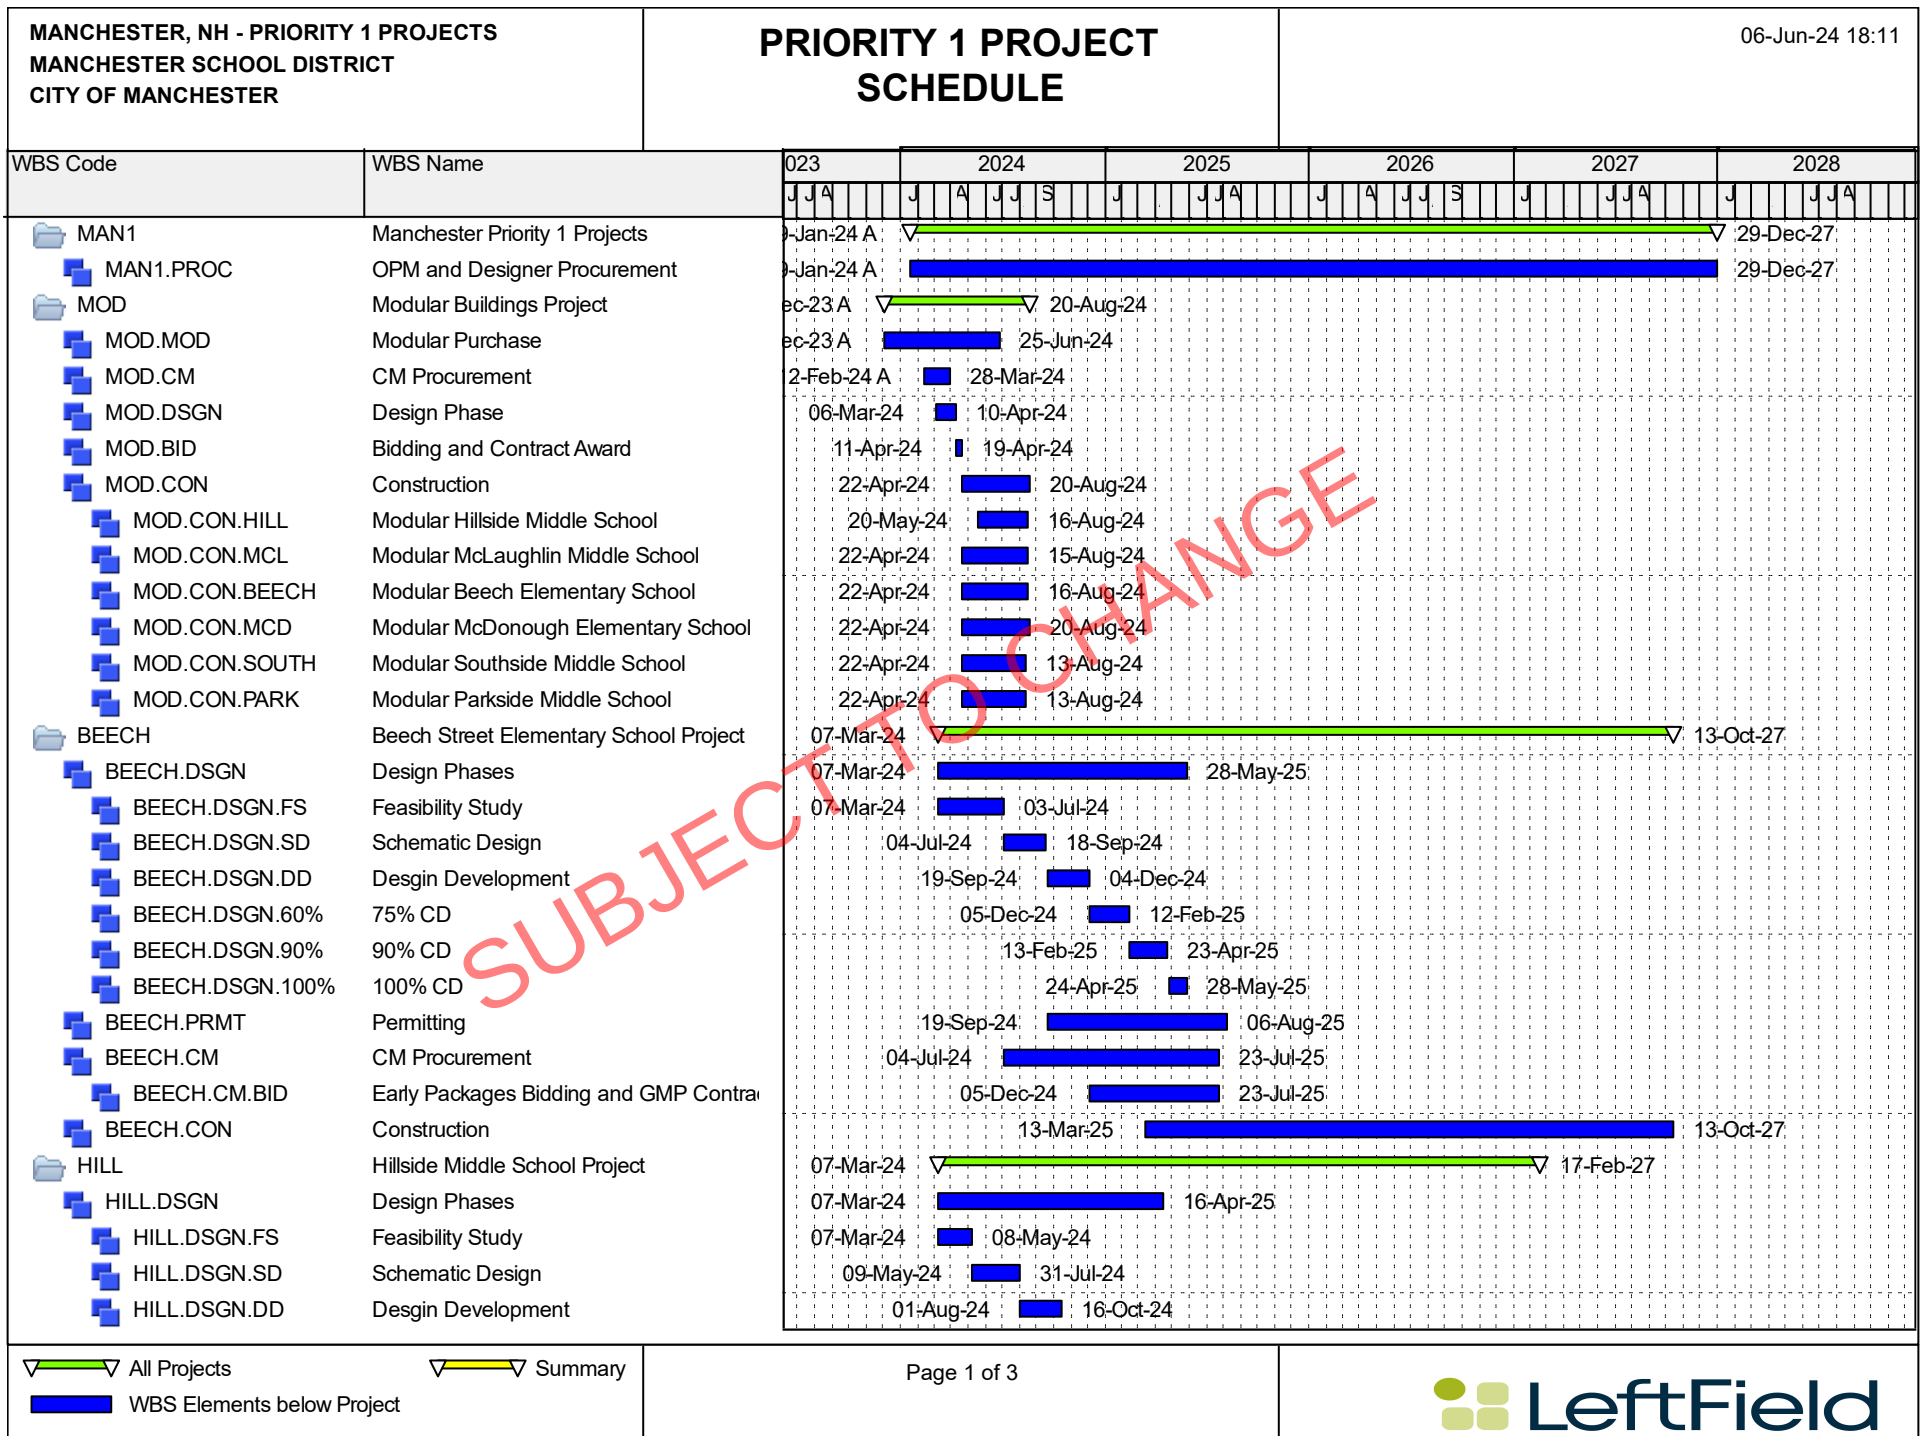

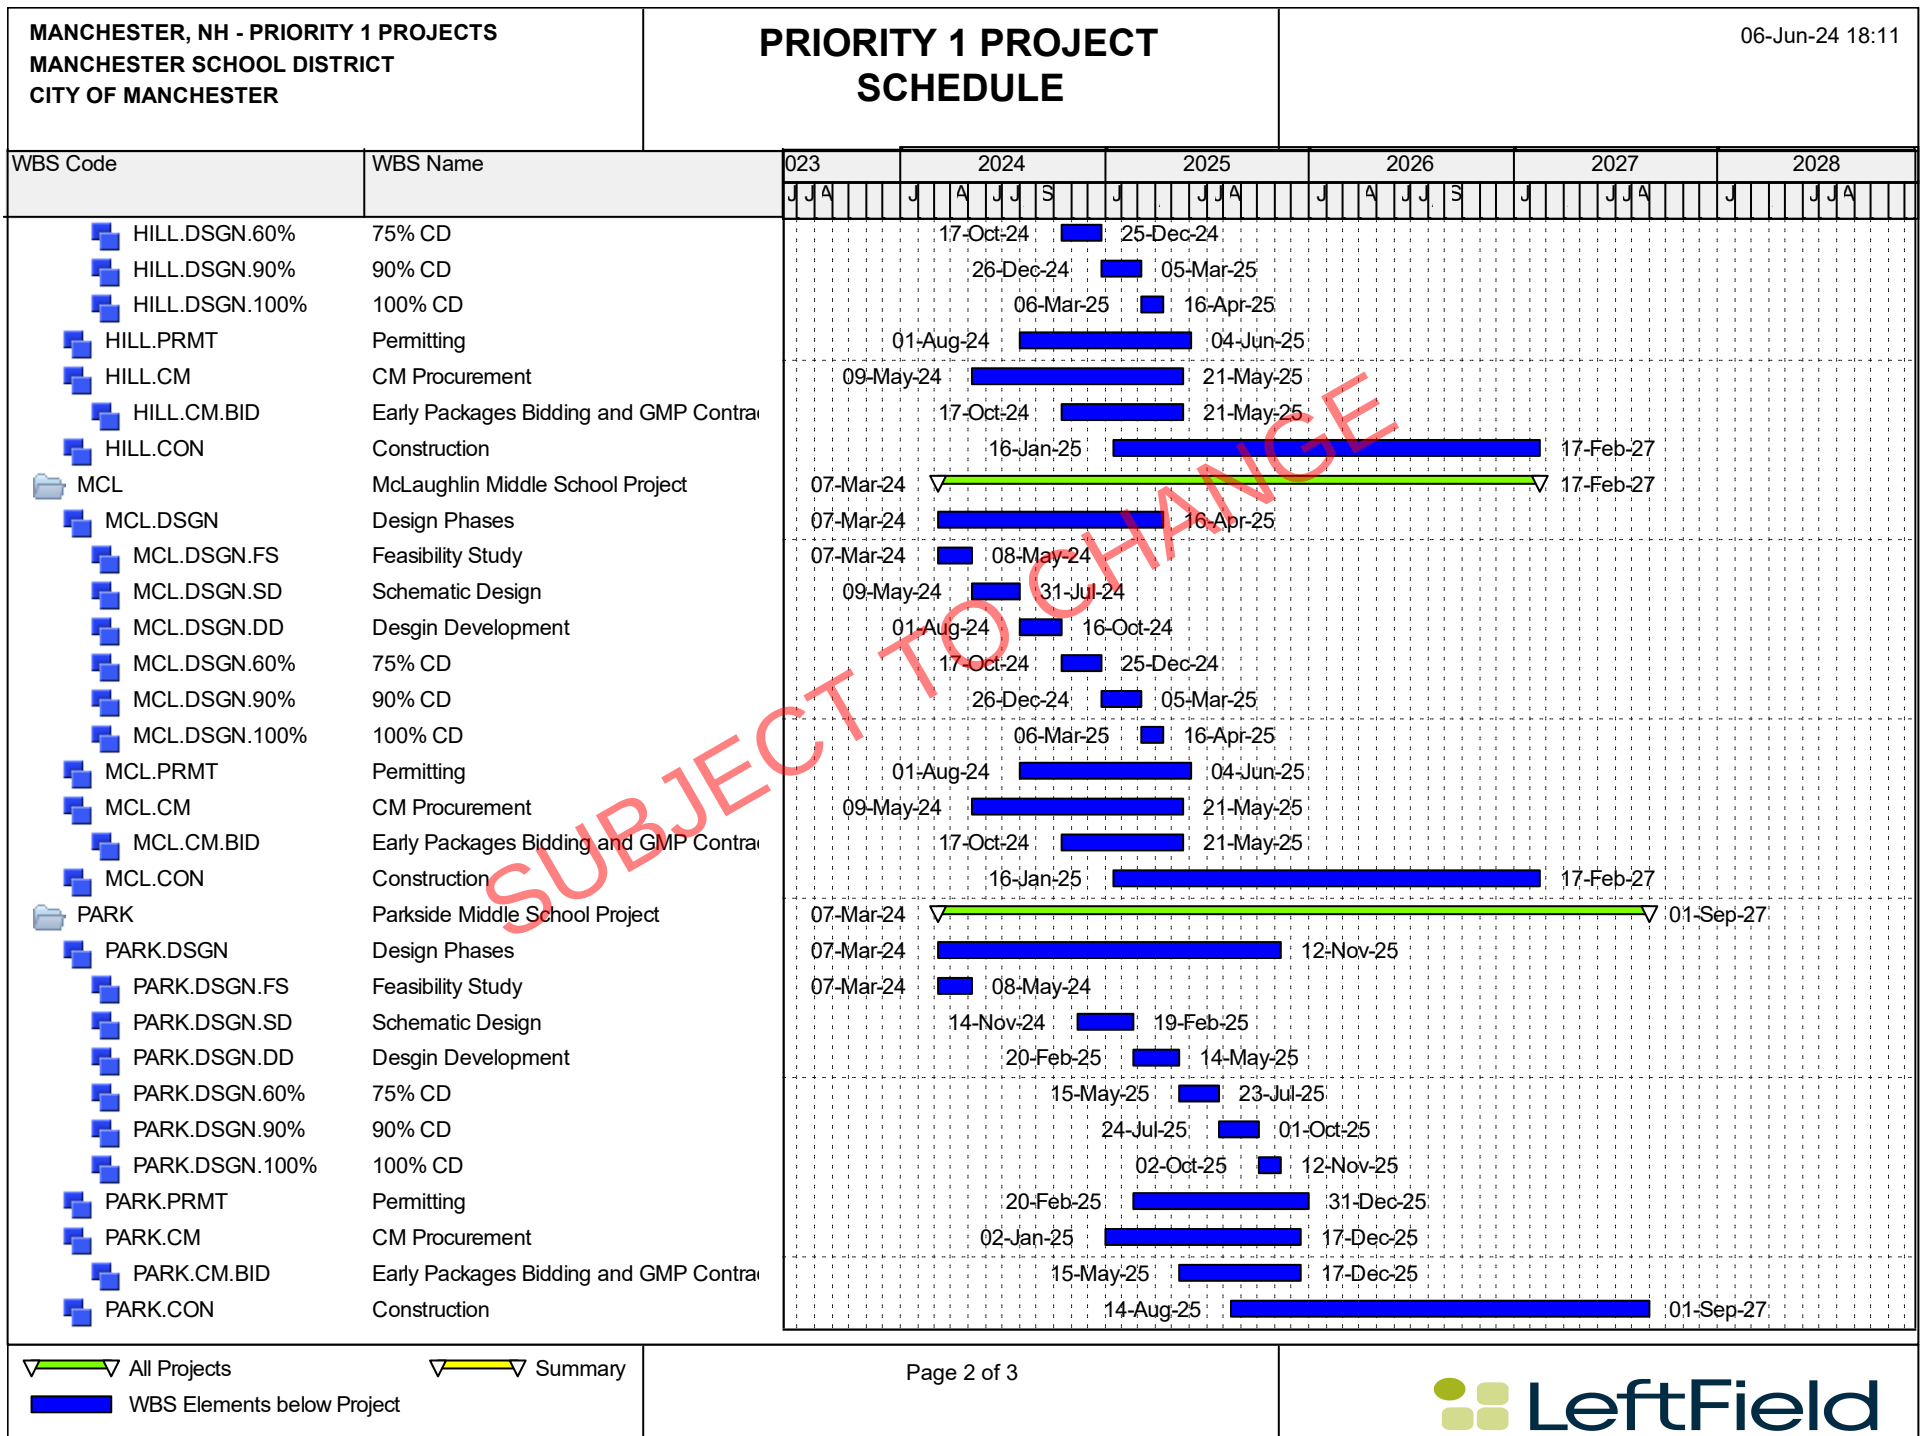


Activity	Start Date	End Date
07-Mar-24	07-Mar-24	12-Nov-25
07-Mar-24	07-Mar-24	12-Nov-25
07-Mar-24	08-May-24	12-Nov-25
14-Nov-24	14-Nov-24	19-Feb-25
20-Feb-25	20-Feb-25	14-May-25
15-May-25	15-May-25	23-Jul-25
24-Jul-25	24-Jul-25	01-Oct-25
02-Oct-25	02-Oct-25	12-Nov-25
20-Feb-25	20-Feb-25	31-Dec-25
02-Jan-25	02-Jan-25	17-Dec-25
15-May-25	15-May-25	17-Dec-25
14-Aug-25	14-Aug-25	17-Dec-25

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

MODULAR BUILDING PROJECT
SCHEDULE

06-Jun-24 17:36

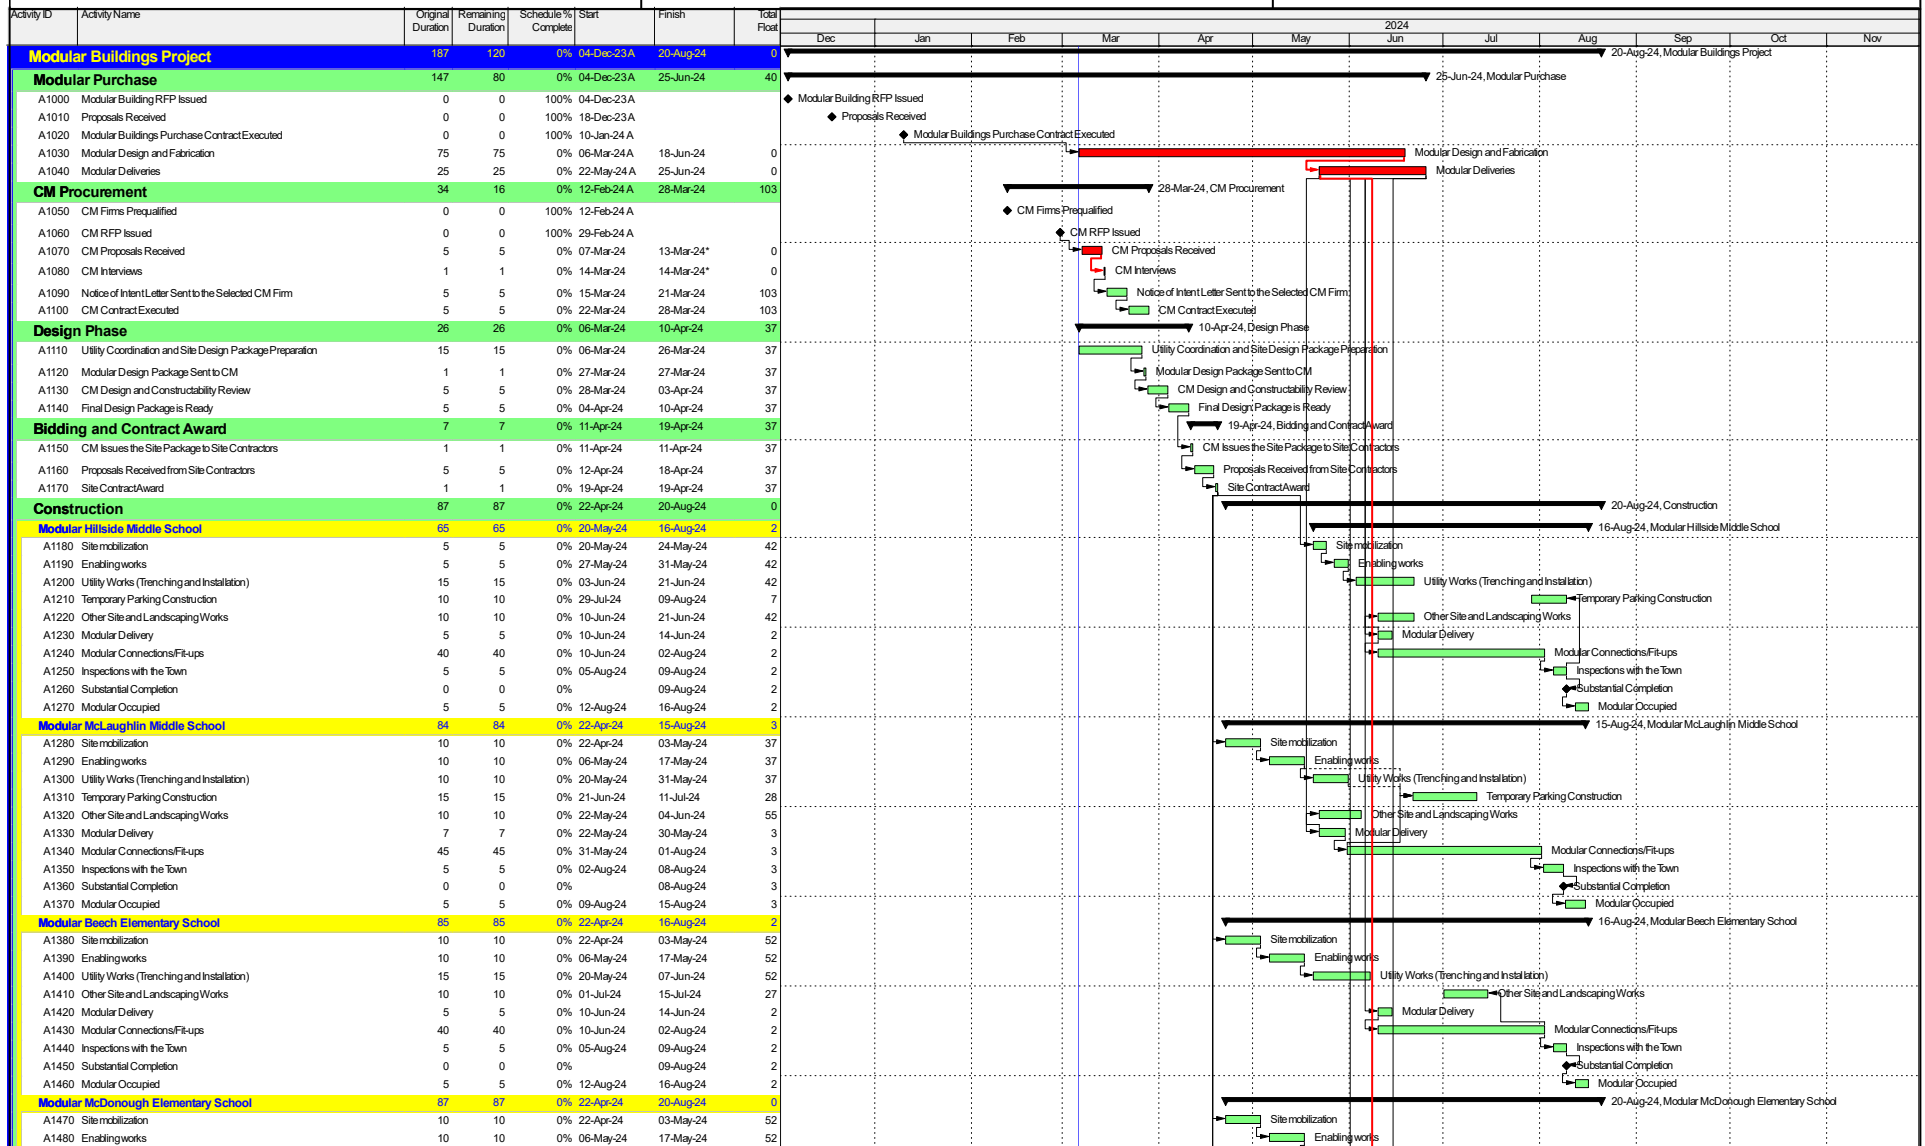


■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone
➤ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

MODULAR BUILDING PROJECT
SCHEDULE

06-Jun-24 17:36

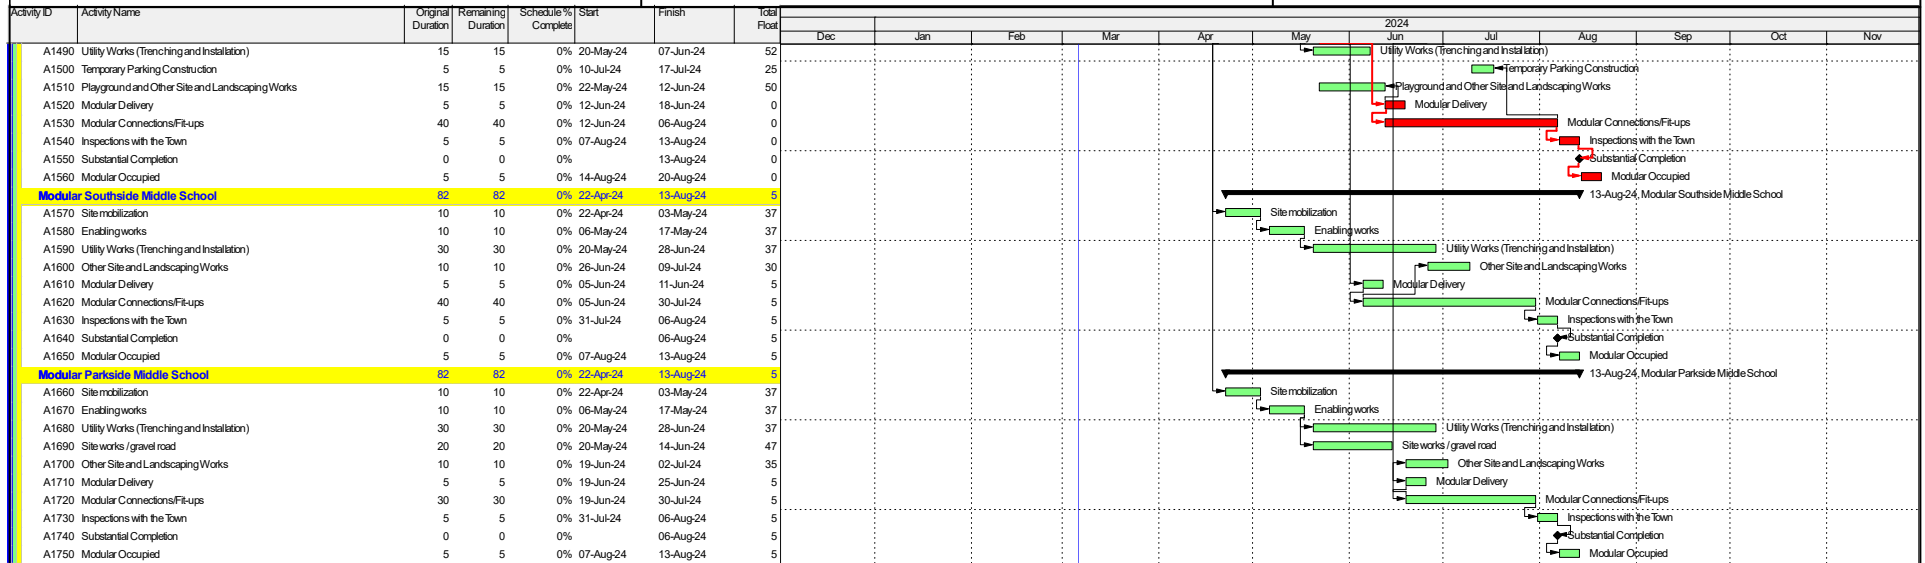


Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone
 Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

**BEECH STREET ELEMENTARY
SCHOOL PROJECT SCHEDULE**

06-Jun-24 17:51

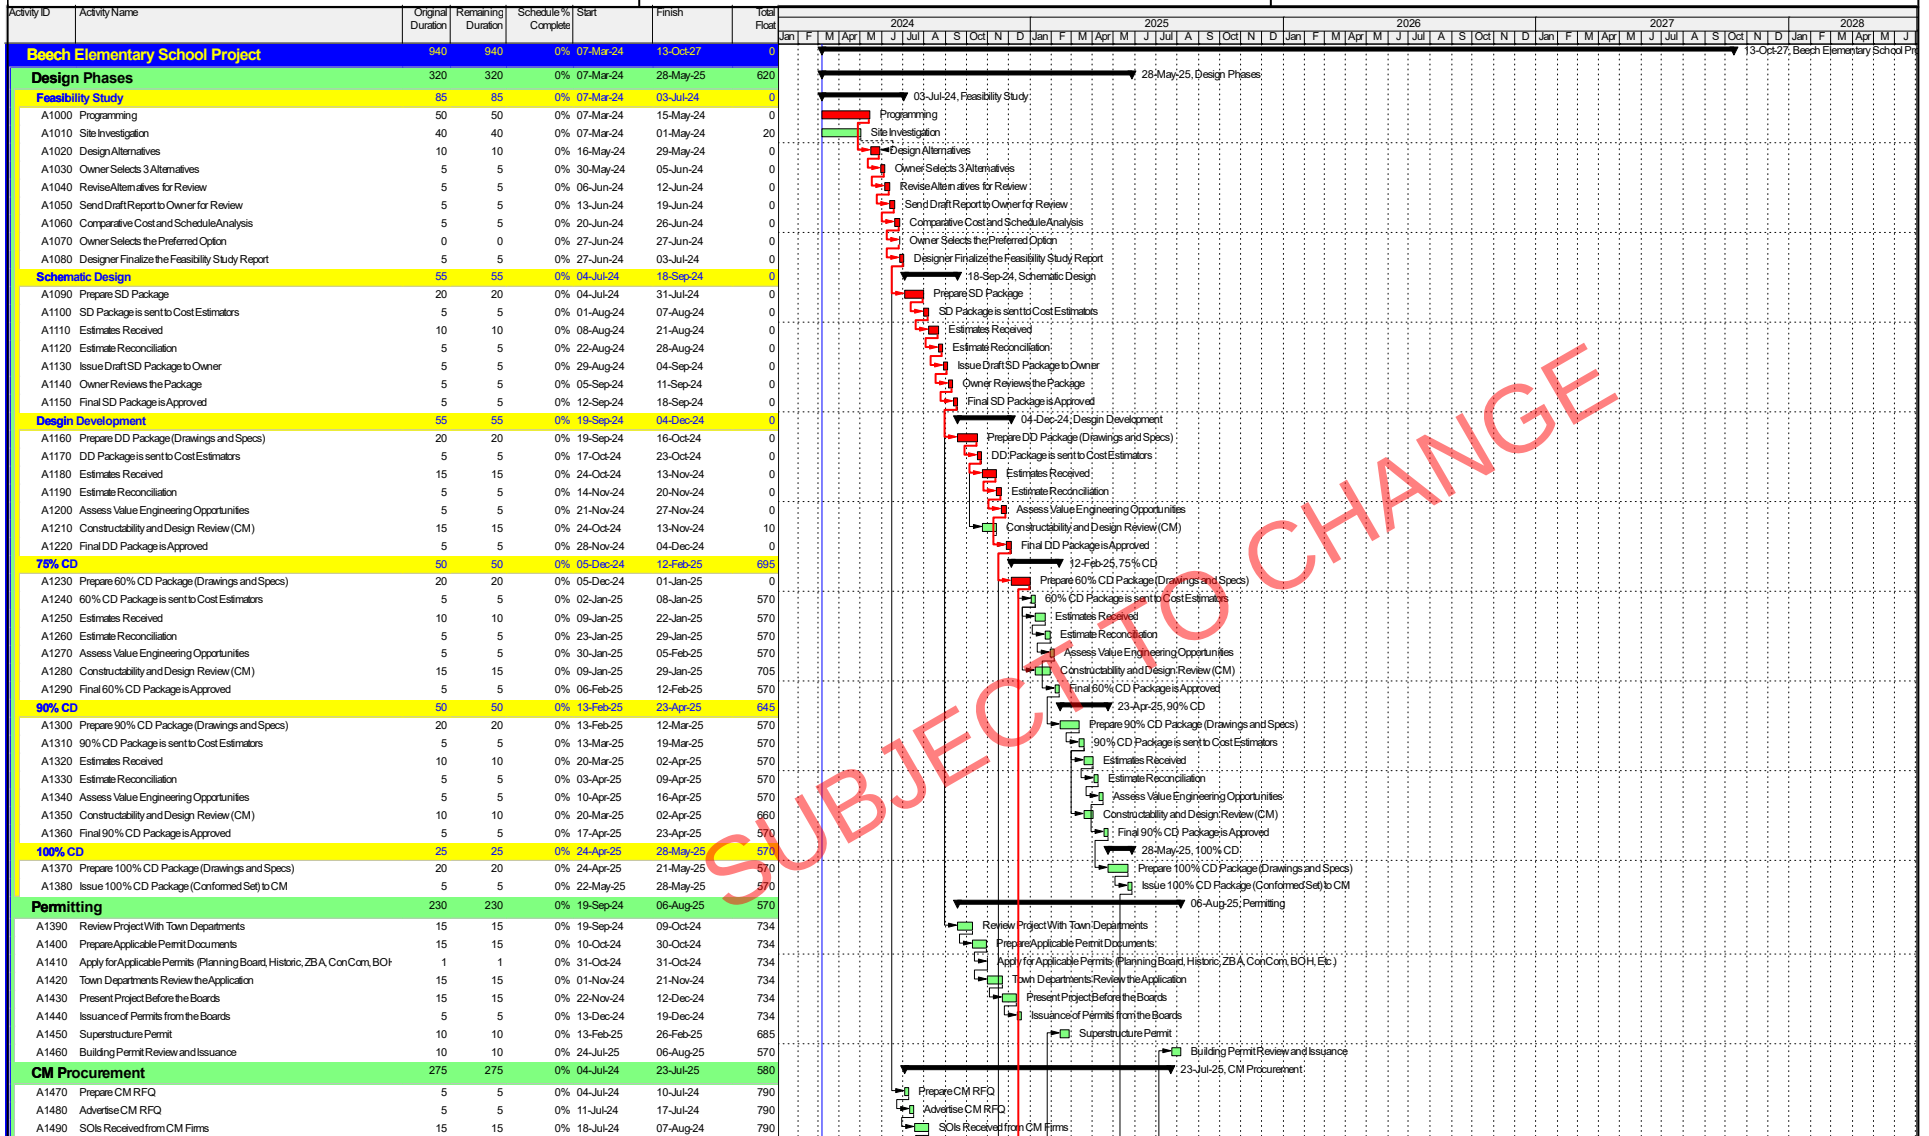


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work

◆ Milestone
 ▶ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

BEECH STREET ELEMENTARY
SCHOOL PROJECT SCHEDULE

06-Jun-24 17:51

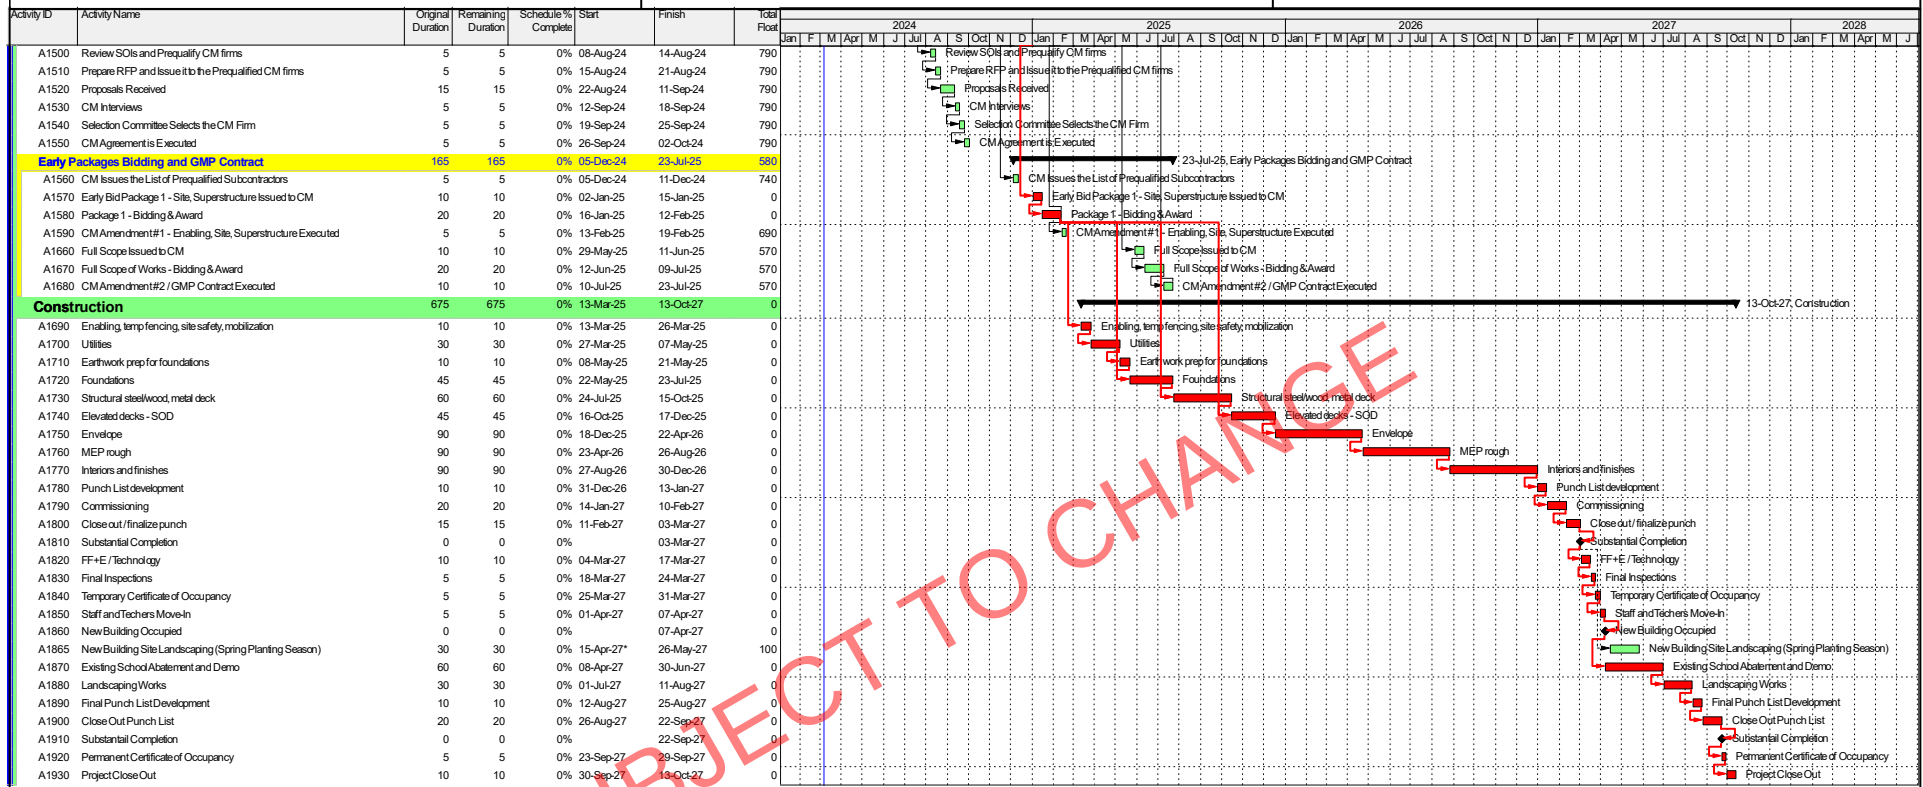


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ➡ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

HILLSIDE MIDDLE SCHOOL PROJECT
SCHEDULE

06-Jun-24 17:56

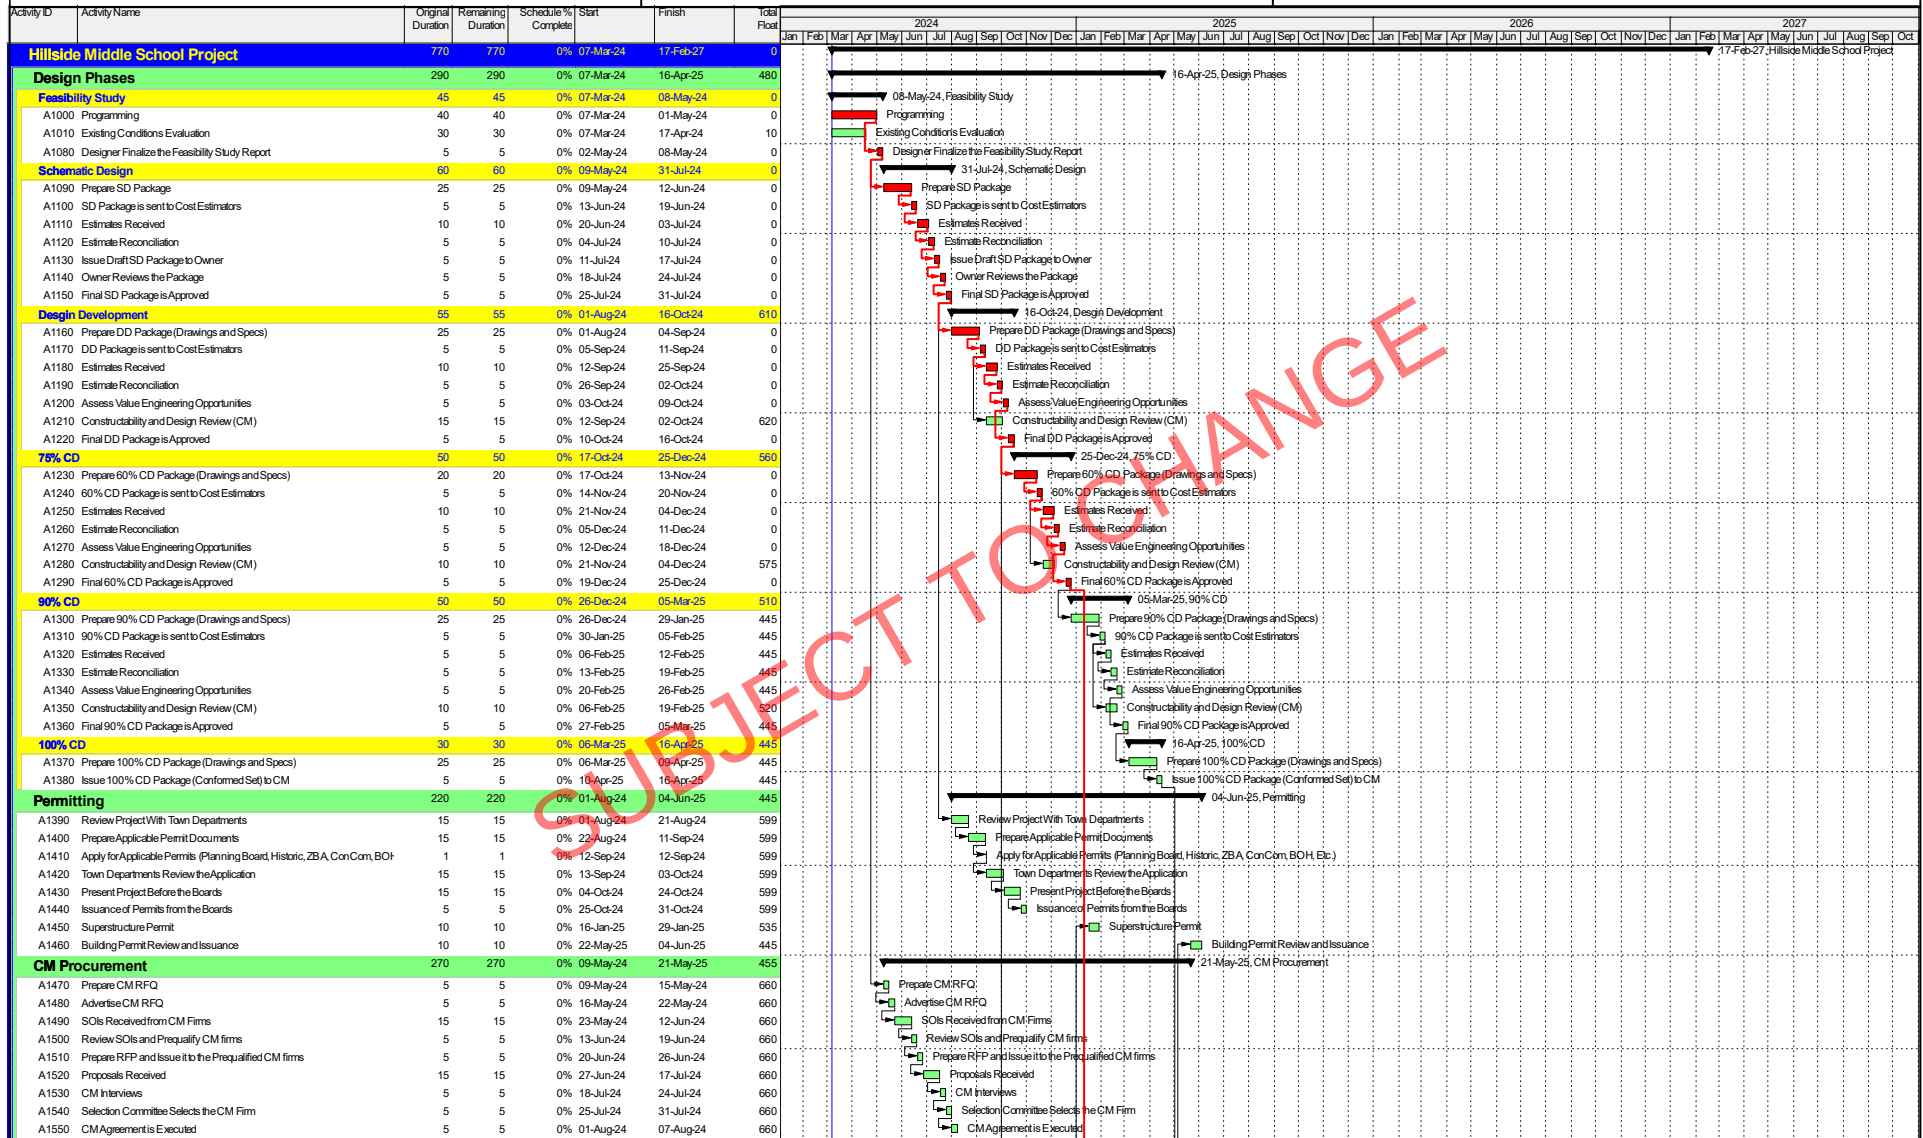


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ➔ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

HILLSIDE MIDDLE SCHOOL PROJECT
SCHEDULE

06-Jun-24 17:56

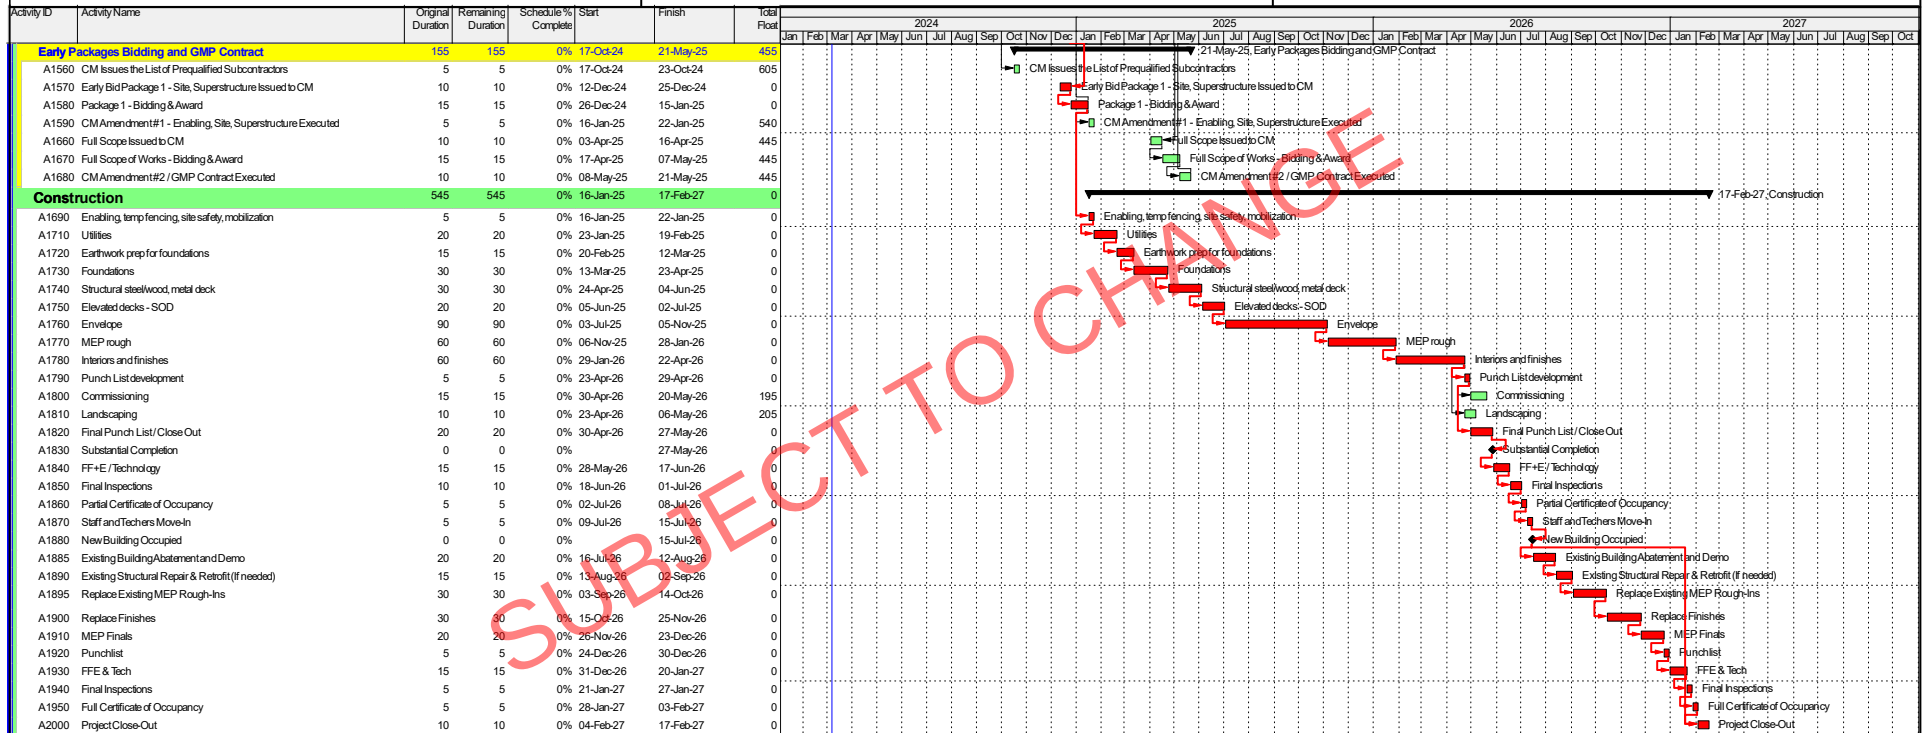

■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work
 ◆ Milestone
 ➡ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

**MCLAUGHLIN MIDDLE
SCHOOL PROJECT SCHEDULE**

06-Jun-24 17:59

Activity ID	Activity Name	Original Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	
								2024 Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec 2025 Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec 2026 Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec 2027 Jan Feb Mar Apr May Jun Jul Aug Sep Oct
McLaughlin Middle School Project								17-Feb-27, McLaughlin Middle School Project
Design Phases								16-Apr-25, Design Phases
Feasibility Study								08-May-24, Feasibility Study
A1000	Programming	40	40	0%	07-Mar-24	01-May-24	0	Programming
A1010	Existing Conditions Evaluation	30	30	0%	07-Mar-24	17-Apr-24	10	Existing Conditions Evaluation
A1080	Designer Finalize the Feasibility Study Report	5	5	0%	02-May-24	08-May-24	0	Designer Finalize the Feasibility Study Report
Schematic Design								31-Jul-24, Schematic Design
A1090	Prepare SD Package	25	25	0%	09-May-24	12-Jun-24	0	Prepare SD Package
A1100	SD Package is sent to Cost Estimators	5	5	0%	13-Jun-24	19-Jun-24	0	SD Package is sent to Cost Estimators
A1110	Estimates Received	10	10	0%	20-Jun-24	03-Jul-24	0	Estimates Received
A1120	Estimate Reconciliation	5	5	0%	04-Jul-24	10-Jul-24	0	Estimate Reconciliation
A1130	Issue Draft SD Package to Owner	5	5	0%	11-Jul-24	17-Jul-24	0	Issue Draft SD Package to Owner
A1140	Owner Reviews the Package	5	5	0%	18-Jul-24	24-Jul-24	0	Owner Reviews the Package
A1150	Final SD Package is Approved	5	5	0%	25-Jul-24	31-Jul-24	0	Final SD Package is Approved
Design Development								16-Oct-24, Design Development
A1160	Prepare DD Package (Drawings and Specs)	25	25	0%	01-Aug-24	04-Sep-24	0	Prepare DD Package (Drawings and Specs)
A1170	DD Package is sent to Cost Estimators	5	5	0%	05-Sep-24	11-Sep-24	0	DD Package is sent to Cost Estimators
A1180	Estimates Received	10	10	0%	12-Sep-24	25-Sep-24	0	Estimates Received
A1190	Estimate Reconciliation	5	5	0%	26-Sep-24	02-Oct-24	0	Estimate Reconciliation
A1200	Assess Value Engineering Opportunities	5	5	0%	03-Oct-24	09-Oct-24	0	Assess Value Engineering Opportunities
A1210	Constructability and Design Review (CM)	15	15	0%	12-Sep-24	02-Oct-24	620	Constructability and Design Review (CM)
A1220	Final DD Package is Approved	5	5	0%	10-Oct-24	16-Oct-24	0	Final DD Package is Approved
75% CD								25-Dec-24, 75% CD
A1230	Prepare 60% CD Package (Drawings and Specs)	20	20	0%	17-Oct-24	13-Nov-24	0	Prepare 60% CD Package (Drawings and Specs)
A1240	60% CD Package is sent to Cost Estimators	5	5	0%	14-Nov-24	20-Nov-24	0	60% CD Package is sent to Cost Estimators
A1250	Estimates Received	10	10	0%	21-Nov-24	04-Dec-24	0	Estimates Received
A1260	Estimate Reconciliation	5	5	0%	05-Dec-24	11-Dec-24	0	Estimate Reconciliation
A1270	Assess Value Engineering Opportunities	5	5	0%	12-Dec-24	18-Dec-24	0	Assess Value Engineering Opportunities
A1280	Constructability and Design Review (CM)	10	10	0%	21-Nov-24	04-Dec-24	575	Constructability and Design Review (CM)
A1290	Final 60% CD Package is Approved	5	5	0%	19-Dec-24	25-Dec-24	0	Final 60% CD Package is Approved
90% CD								05-Mar-25, 90% CD
A1300	Prepare 90% CD Package (Drawings and Specs)	25	25	0%	26-Dec-24	29-Jan-25	445	Prepare 90% CD Package (Drawings and Specs)
A1310	90% CD Package is sent to Cost Estimators	5	5	0%	30-Jan-25	05-Feb-25	445	90% CD Package is sent to Cost Estimators
A1320	Estimates Received	5	5	0%	06-Feb-25	12-Feb-25	445	Estimates Received
A1330	Estimate Reconciliation	5	5	0%	13-Feb-25	19-Feb-25	445	Estimate Reconciliation
A1340	Assess Value Engineering Opportunities	5	5	0%	20-Feb-25	26-Feb-25	445	Assess Value Engineering Opportunities
A1350	Constructability and Design Review (CM)	10	10	0%	06-Feb-25	19-Feb-25	520	Constructability and Design Review (CM)
A1360	Final 90% CD Package is Approved	5	5	0%	27-Feb-25	05-Mar-25	445	Final 90% CD Package is Approved
100% CD								16-Apr-25, 100% CD
A1370	Prepare 100% CD Package (Drawings and Specs)	25	25	0%	06-Mar-25	09-Apr-25	445	Prepare 100% CD Package (Drawings and Specs)
A1380	Issue 100% CD Package (Conformed Set) to CM	5	5	0%	10-Apr-25	16-Apr-25	445	Issue 100% CD Package (Conformed Set) to CM
Permitting								04-Jun-25, Permitting
A1390	Review Project With Town Departments	15	15	0%	01-Aug-24	21-Aug-24	599	Review Project With Town Departments
A1400	Prepare Applicable Permit Documents	15	15	0%	22-Aug-24	11-Sep-24	599	Prepare Applicable Permit Documents
A1410	Apply for Applicable Permits (Planning Board, Historic, ZBA, ConCom, BOH)	1	1	0%	12-Sep-24	12-Sep-24	599	Apply for Applicable Permits (Planning Board, Historic, ZBA, ConCom, BOH, Etc.)
A1420	Town Departments Review the Application	15	15	0%	13-Sep-24	03-Oct-24	599	Town Departments Review the Application
A1430	Present Project Before the Boards	15	15	0%	04-Oct-24	24-Oct-24	599	Present Project Before the Boards
A1440	Issuance of Permits from the Boards	5	5	0%	25-Oct-24	31-Oct-24	599	Issuance of Permits from the Boards
A1450	Superstructure Permit	10	10	0%	16-Jan-25	29-Jan-25	535	Superstructure Permit
A1460	Building Permit Review and Issuance	10	10	0%	22-May-25	04-Jun-25	445	Building Permit Review and Issuance
CM Procurement								21-May-25, CM Procurement
A1470	Prepare CM RFQ	5	5	0%	09-May-24	15-May-24	660	Prepare CM RFQ
A1480	Advertise CM RFQ	5	5	0%	16-May-24	22-May-24	660	Advertise CM RFQ
A1490	SOs Received from CM Firms	15	15	0%	23-May-24	12-Jun-24	660	SOs Received from CM Firms
A1500	Review SOs and Prequalify CM firms	5	5	0%	13-Jun-24	19-Jun-24	660	Review SOs and Prequalify CM firms
A1510	Prepare RFP and Issue it to the Prequalified CM firms	5	5	0%	20-Jun-24	26-Jun-24	660	Prepare RFP and Issue it to the Prequalified CM firms
A1520	Proposals Received	15	15	0%	27-Jun-24	17-Jul-24	660	Proposals Received
A1530	CM Interviews	5	5	0%	18-Jul-24	24-Jul-24	660	CM Interviews
A1540	Selection Committee Selects the CM Firm	5	5	0%	25-Jul-24	31-Jul-24	660	Selection Committee Selects the CM Firm
A1550	CM Agreement is Executed	5	5	0%	01-Aug-24	07-Aug-24	660	CM Agreement is Executed


Actual Work
 Remaining Work
 Critical Remaining Work

Milestone
 Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

MCLAUGHLIN MIDDLE
SCHOOL PROJECT SCHEDULE

06-Jun-24 17:59


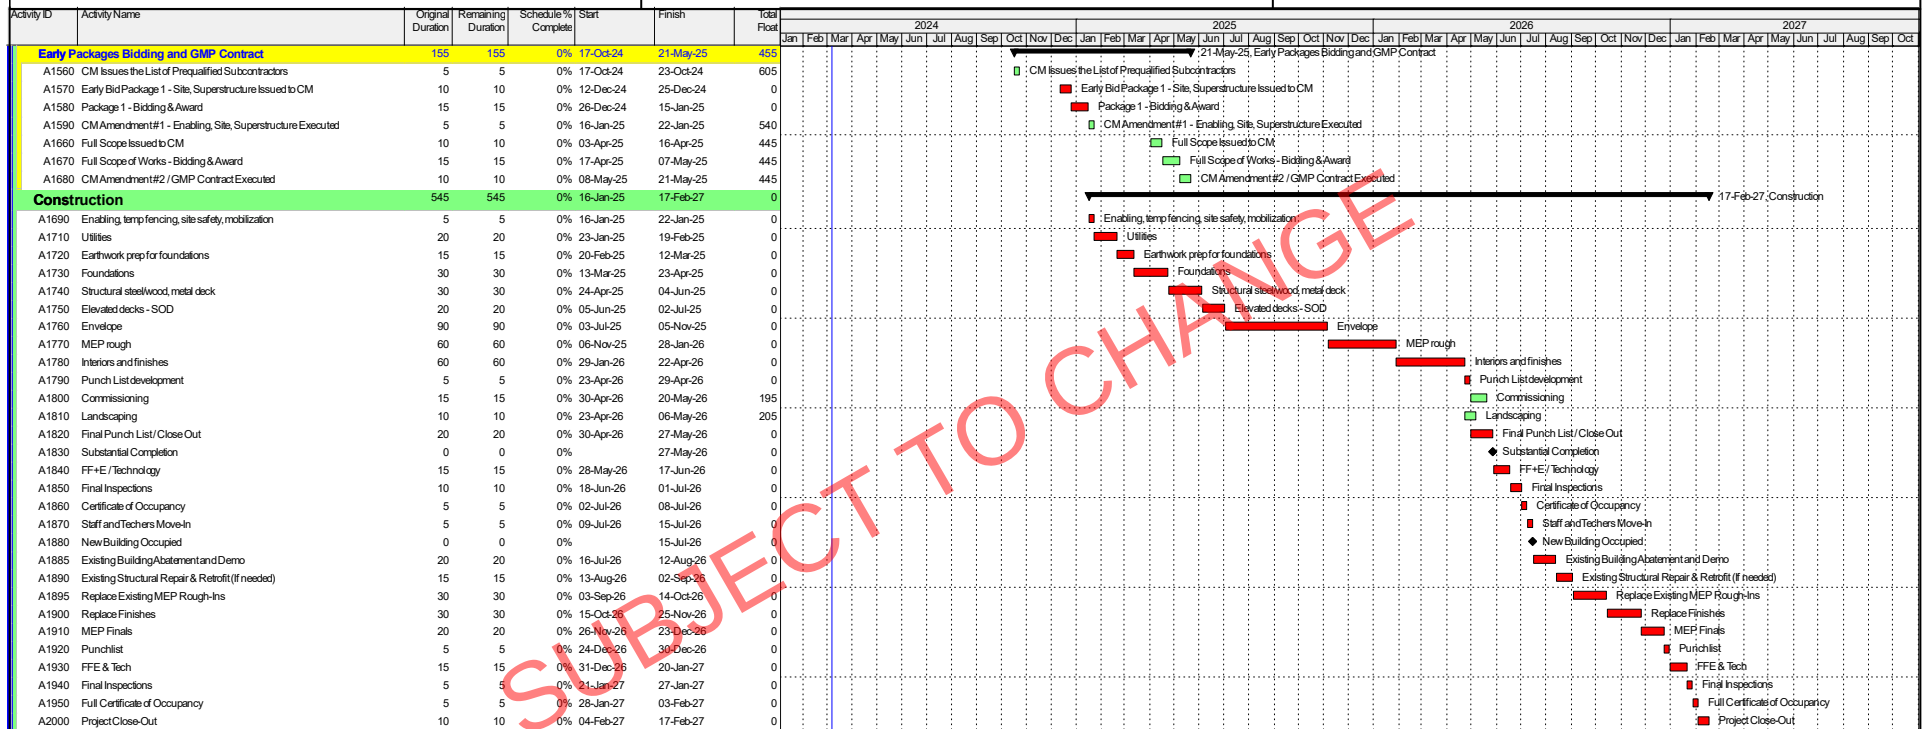


■ Actual Work ◆ Milestone
■ Remaining Work ▬ Summary
■ Critical Remaining Work

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

PARKSIDE MIDDLE
SCHOOL PROJECT SCHEDULE



06-Jun-24 18:02

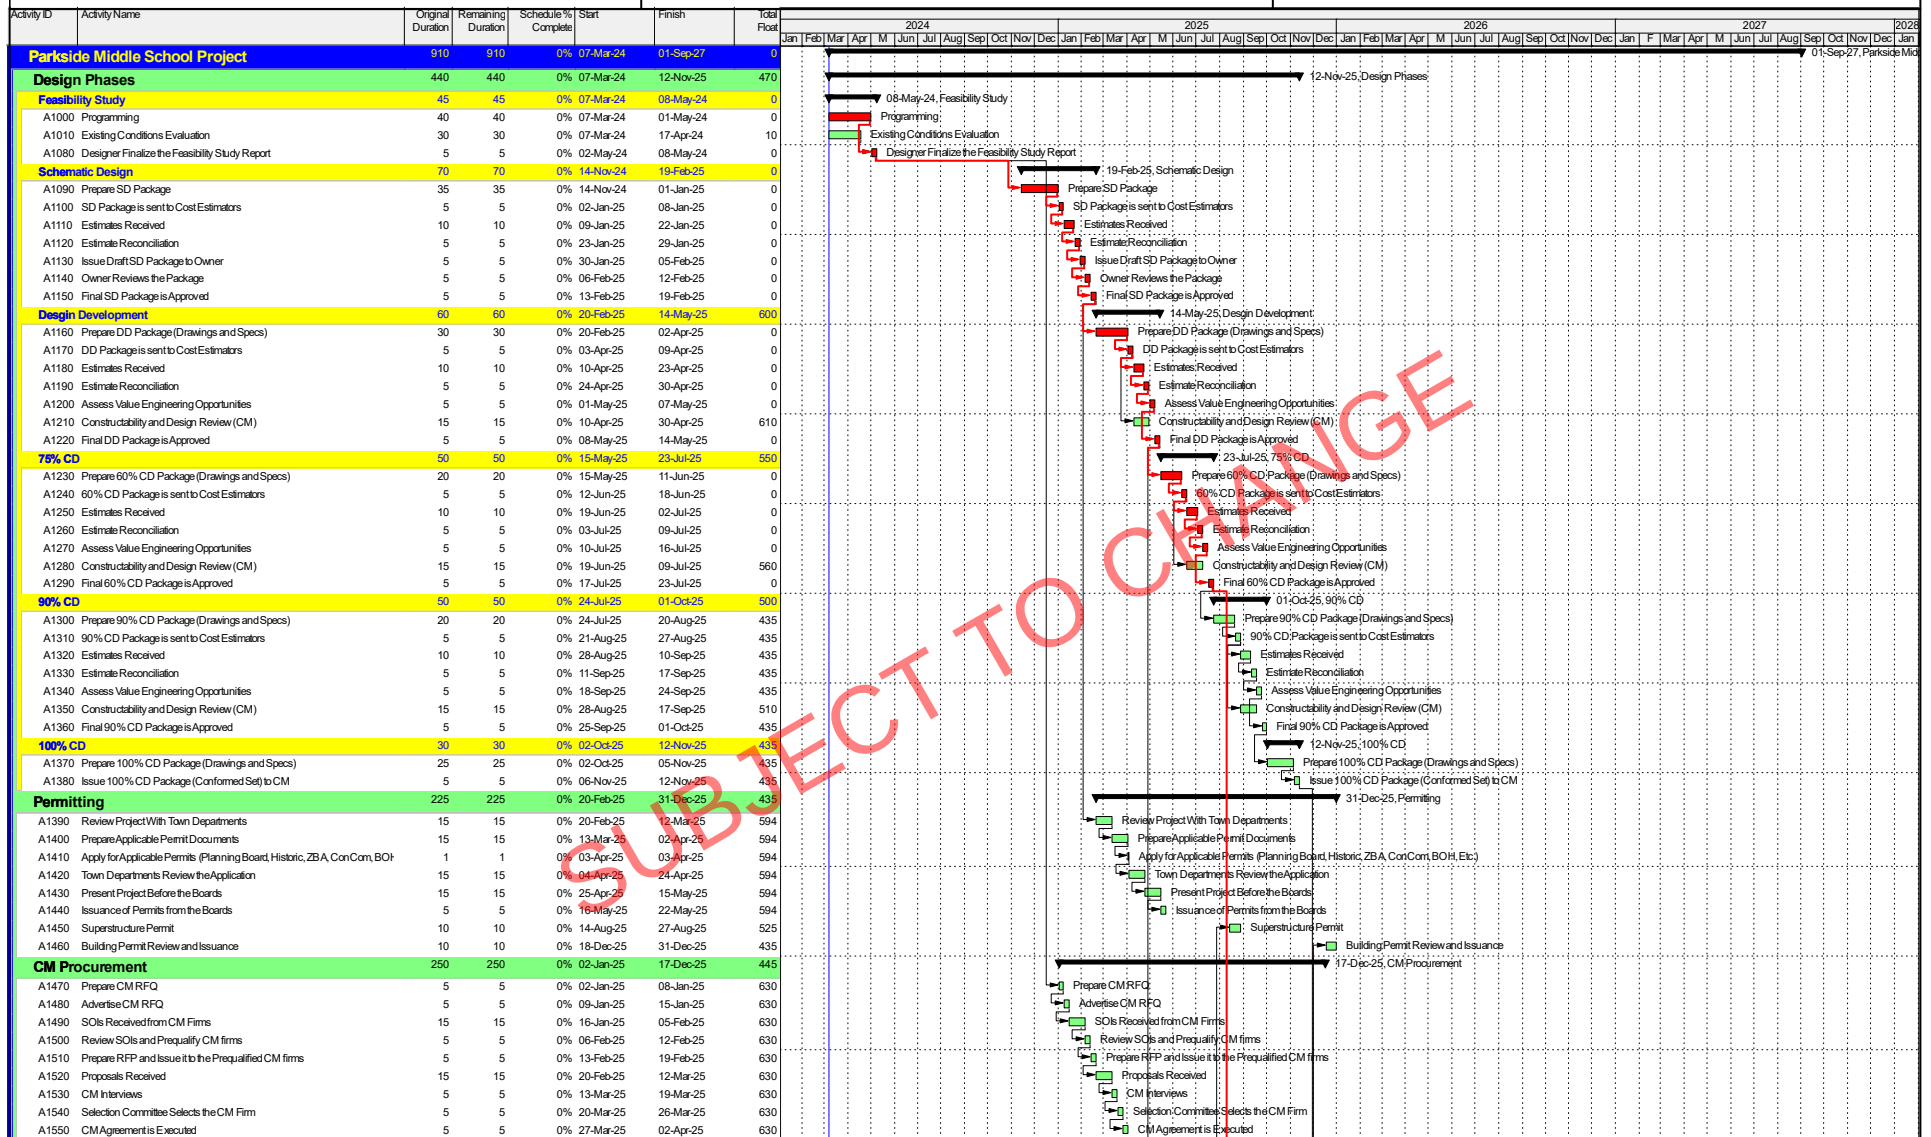

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

PARKSIDE MIDDLE
SCHOOL PROJECT SCHEDULE


06-Jun-24 18:02

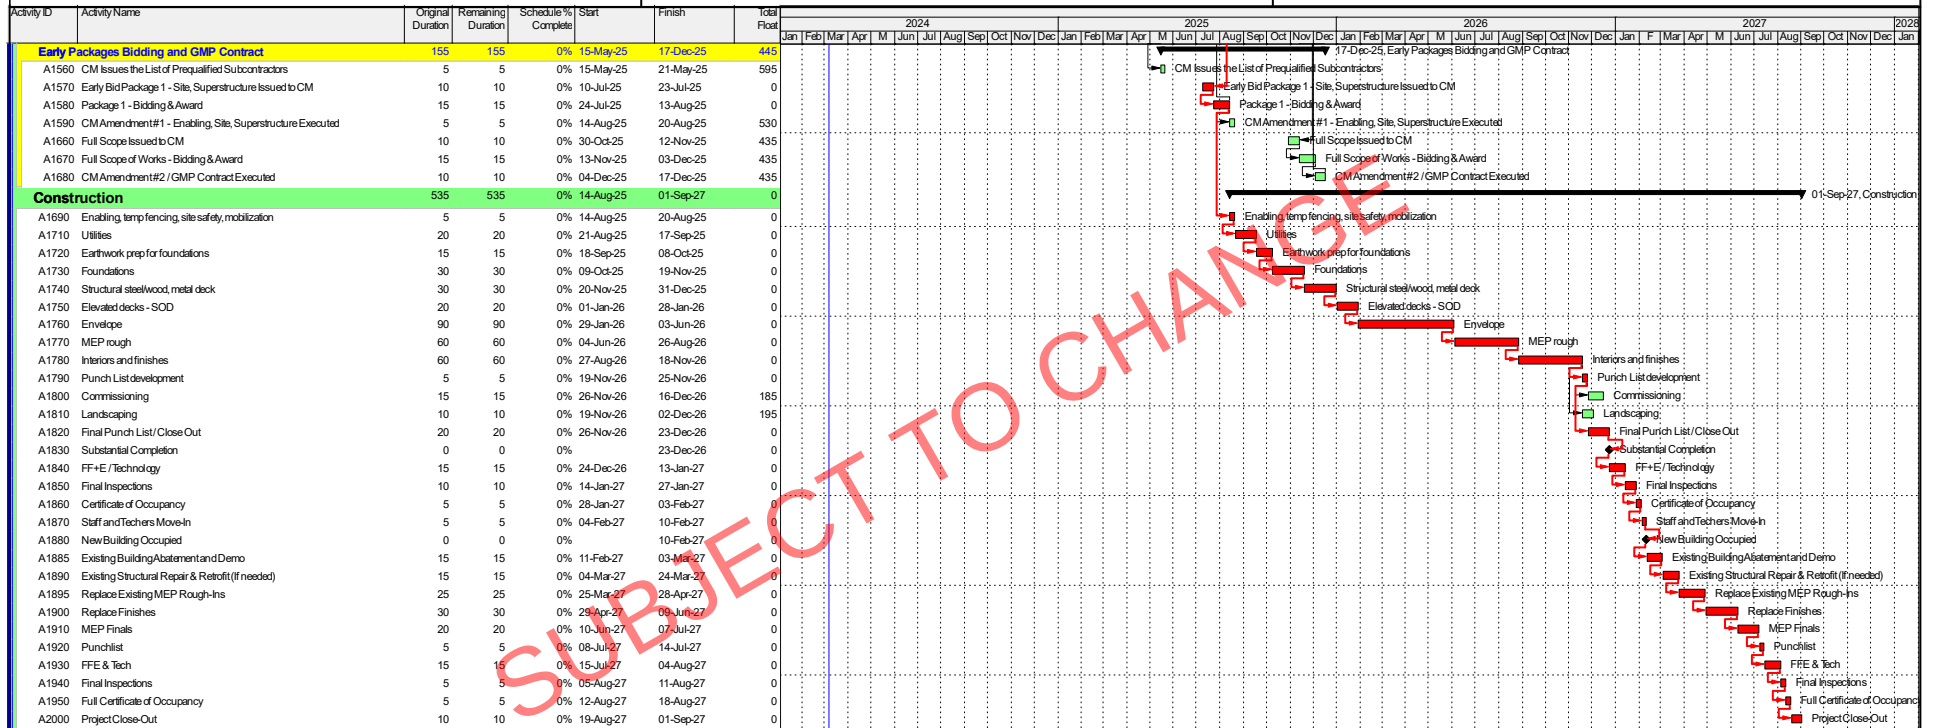

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

SOUTHSIDE MIDDLE
SCHOOL PROJECT SCHEDULE

06-Jun-24 18:04

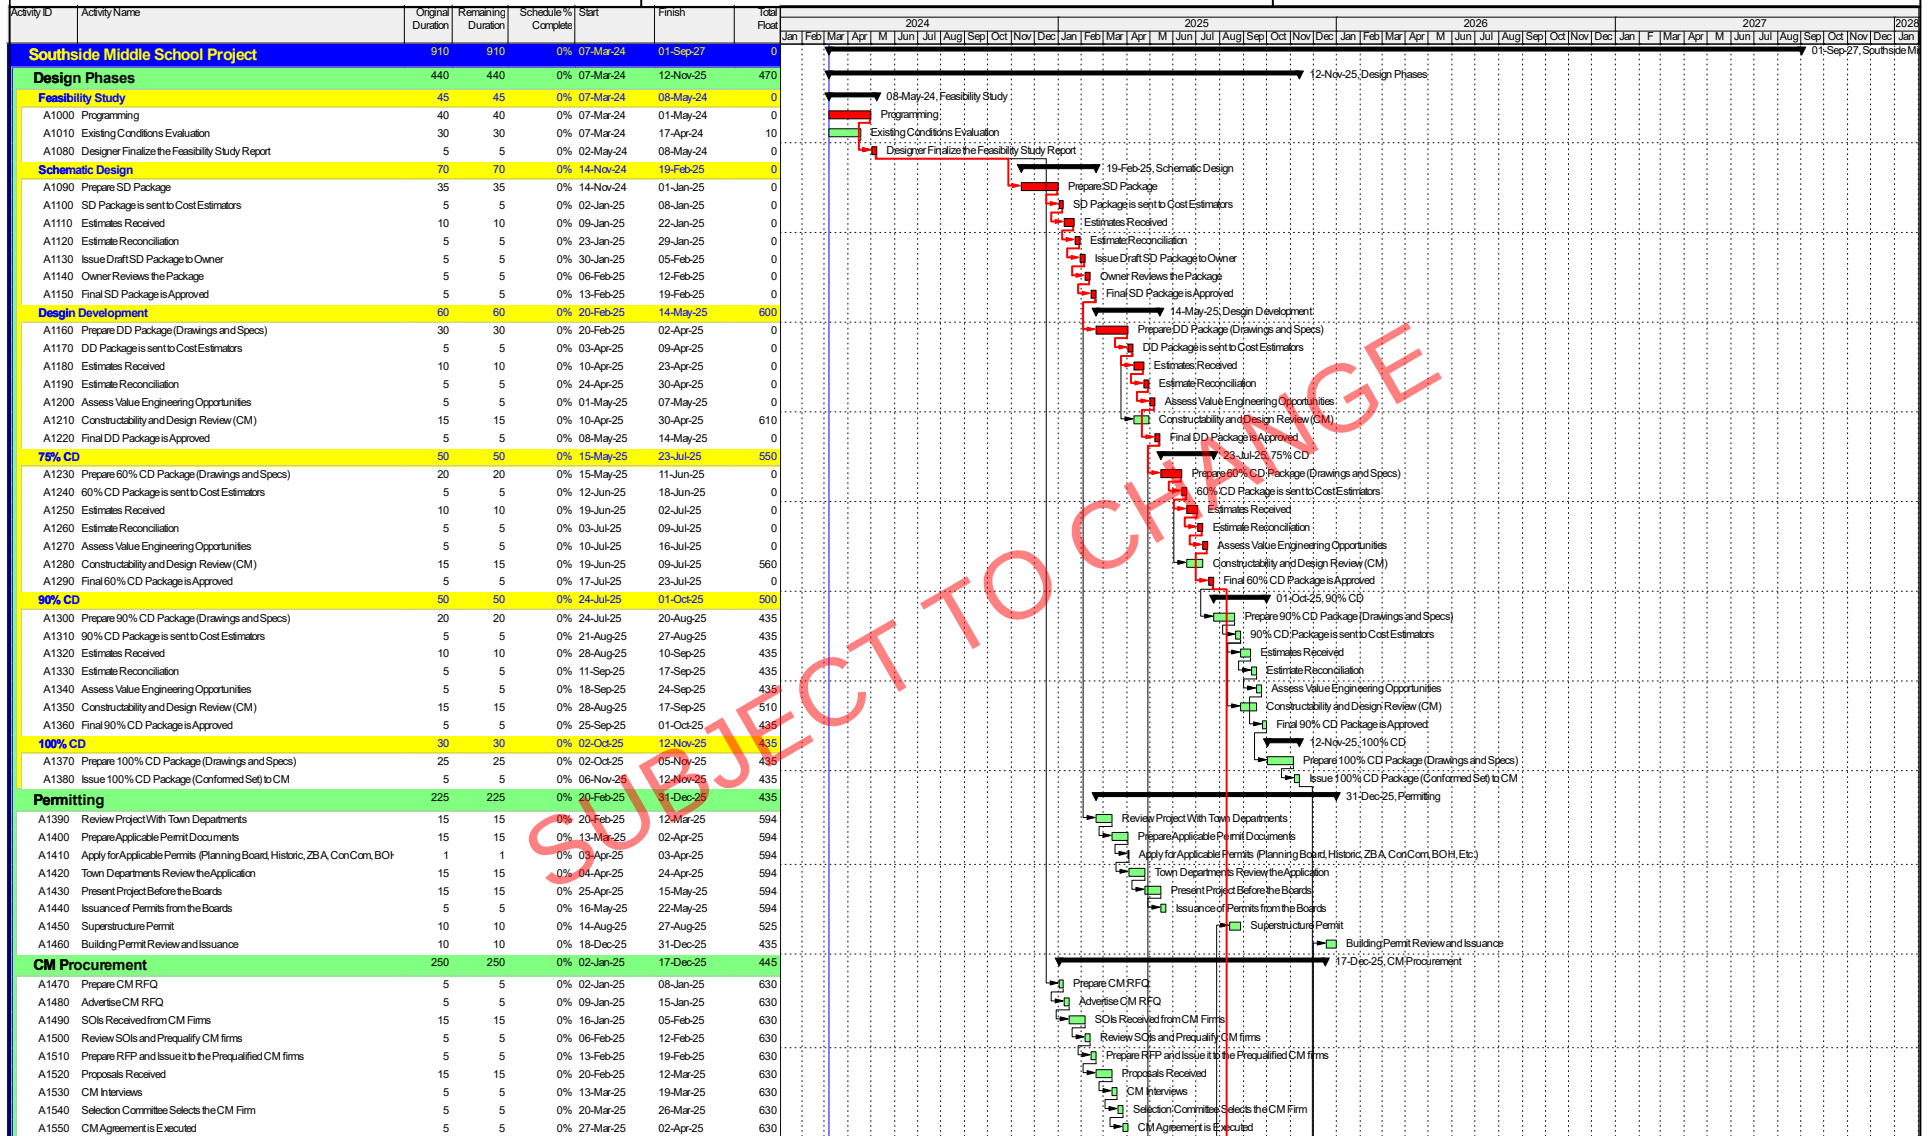


■ Actual Work
 ■ Remaining Work
 ■ Critical Remaining Work

◆ Milestone
 ➔ Summary

MANCHESTER, NH - PRIORITY 1 PROJECT SCHEDULE
MANCHESTER SCHOOL DISTRICT
CITY OF MANCHESTER

SOUTHSIDE MIDDLE
SCHOOL PROJECT SCHEDULE

06-Jun-24 18:04

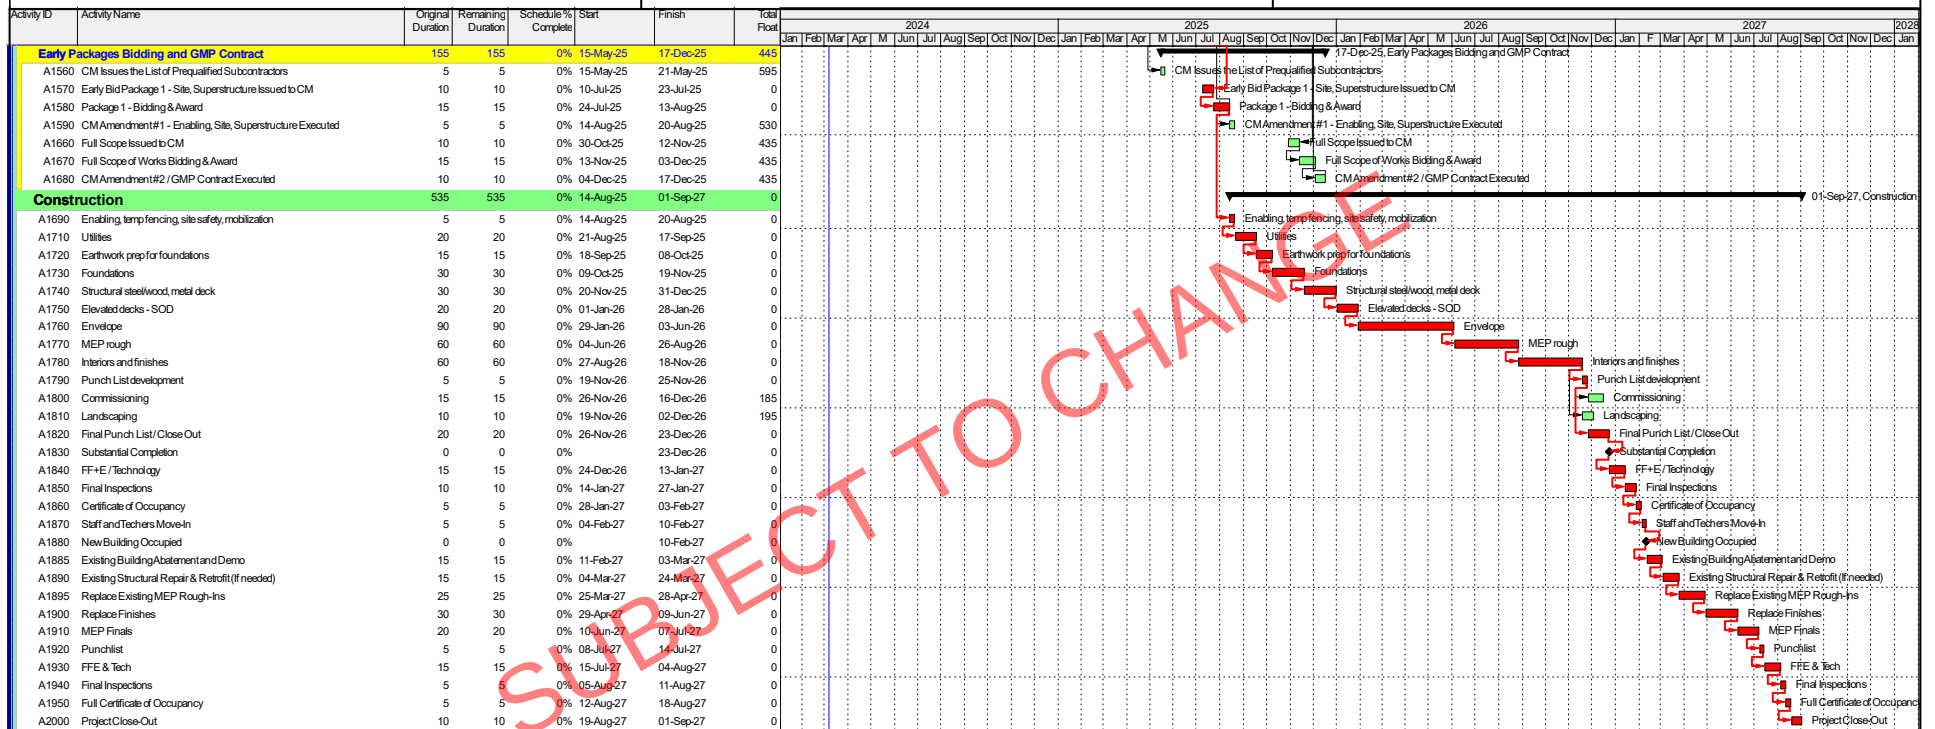

■ Actual Work ◆ Milestone
■ Remaining Work ⇌ Summary
■ Critical Remaining Work
